


# Bond Program Status Report

Through August 2022

### 2014 Bond Program Executive Summary August 2022

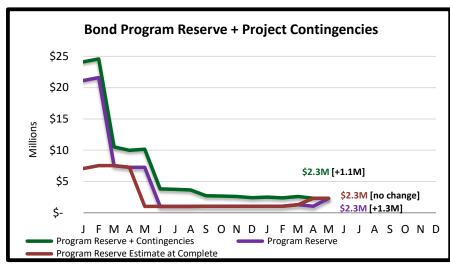

Bond Program Reserve = Funding available to the Bond Program but not yet allocated to a project Project Contingencies = Funding contained within an approved project budget

Bond Program Funding Total		\$ 808,182,088
Revised Approved Current Budget	-	\$ 805,857,896
Bond Program Reserve		\$ 2,324,191
Bond Program Reserve		\$ 2,324,191
Net Contingency Balance	+	\$ -
Bond Program Reserve + Contingencies		\$ 2,324,191
Bond Program Funding Total		\$ 808,182,088
Program Estimate at Complete (EAC)	-	\$ 805,857,896
Projected Program Reserve Estimate at Complete		\$ 2,324,192

### **Budget Perspectivee**

This month the overall Program Reserve is unchanged. Primary cost events were:

- There were no major cost events this month.
- · With the sale of the 2022 bonds we will be spending the 2014 funding allocated for Raleigh Hills as part of the 22 Bond project.
- We are in the process of financially closing out projects from the 2014 bond. Currently we are projecting an additional savings from the District Wide Repairs project.

#### **Schedule Perspective**

- · We are beginning to ramp up towards bidding for the summer 2023 projects, we are expecting to see significant cost escalation.
- Summer project updates: All summer projects are tracking well for completion. Two projects (Bethany Roof/Seismic & ISB Modular Roof) are currently behind schedule due to significant unforeseen conditions. They will each be complete by mid-late September.

#### **Challenges and Opportunities**

• We are seeing unprecedented levels of material cost escalation as well as very long lead times. We have been working to extend our project planning cycles to account for these delays.

### 2014 Bond Program Scorecard August 2022

Performance Key

Green = On Track
Yellow = Watchlist

Red = Trouble

Gray = Milestone Complete

(Date) = Target


Date = Actual

N/A = Not Applicable

Current Performance Metrics	Bethany HVAC & Roof	ISB Roof & HVAC	2021 Roofs (Montclair)	Security Upgrades: Classroom Walls	Vose Classroom Addition	2022 Repipes	2022 HVAC Uprades Group 1
Overall Budget Performance	On Track	On Track	On Track	On Track	On Track	On Track	On Track
Budget Percent Complete	38.00%	66.00%	64.00%	25.00%	15.00%	2.00%	4.00%
Overall Schedule Performance	On Track	On Track	On Track	On Track	On Track	On Track	On Track
Schedule Percent Complete	43.00%	74.00%	60.00%	30.00%	10.00%	0.00%	0.00%
Schedule Milestones	Bethany HVAC & Roof	ISB Roof & HVAC	2021 Roof Replacements	Security Upgrades: Classroom Walls	Vose Classroom Addition	2022 Repipes	2022 HVAC Uprades Group 1
Design Team Contracted	N/A	8-2020	6-2020	11-2020	11-2020	11-2021	3-2021
Design - Schematic Design	N/A	11-2020	7-2020	1-2021	N/A	11-2021	N/A
Design - Design Development	3-2021	12-2020	9-2020	2-2021	1-2021	1-2022	5-2021
Design - Construction Documents	4-2021	2-2021	10-2020	3-2021	2-2021	(2-2022)	6-2021
Permitting - Land Use	N/A	N/A	N/A	N/A	7-2021	N/A	N/A
Permitting - Site Development	N/A	N/A	N/A	N/A	7-2021	N/A	N/A
Permitting - Building	6-2021	4-2021	11-2020	3-2021	12-2021	(3-2022)	N/A
Construction - Contract Award	10-2020	4-2021	1-2021	6-2021	10-2021	(3-2022)	11-2021
Construction - Start	6-2021	6-2021	(6-2022)	6-2021	(3-2022)	(6-2022)	(6-2022)
Construction - Finish	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(9-2022)	(8-2022)	(8-2022)
Owner Activities - FF&E Ordered	N/A	N/A	N/A	N/A	(1-2022)	N/A	N/A
Owner Activities - FF&E Delivered	N/A	N/A	N/A	N/A	TBD	N/A	N/A
Owner Activities - Occupancy	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(8-2022)	(8-2022)	(8-2022)
Project Complete (Month - Year)	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(9-2022)	(8-2022)	(8-2022)
	T T			1			
Equity Goals				]			
Participation	Target %	Current %	Change %				
MWSDVE - Consultants	10.0%	18.0%	-0.20%				
MWSDVE - Contractors	10.0%	14.6%	-0.10%				
Apprenticeship	10.0%	19.0%	No change				




# 2014 Bond Construction Program Summer 2022 Activity

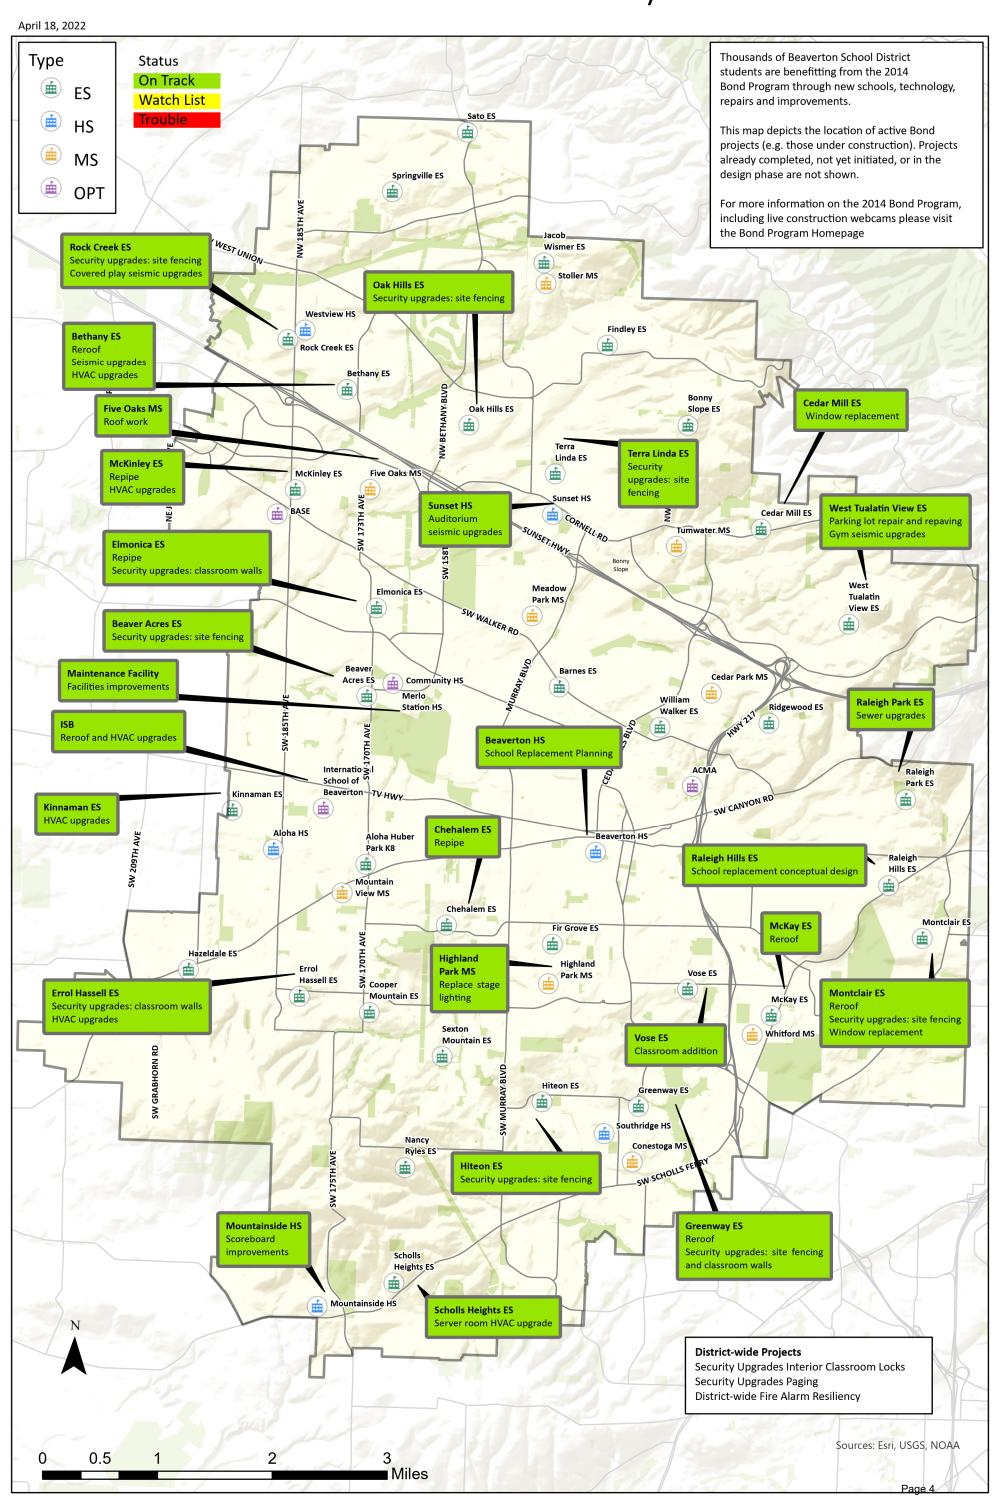


### **2014 Construction Bond Program**

Equity Performance August 2022 Report

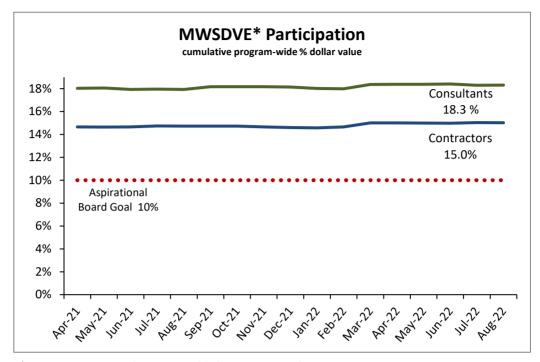

<sup>\*</sup>Minority, Women and Service Disabled Veteran Owned Enterprises

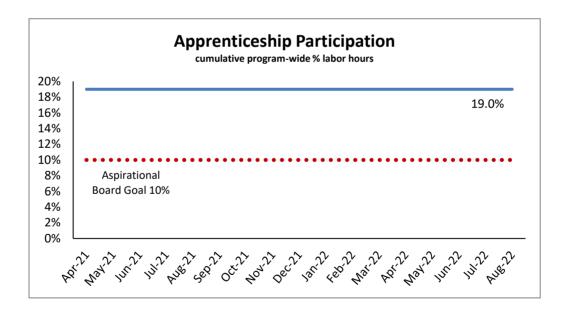

Project List	ginal Budget Allocations	Revised Approve		July-22 Est @ Comp	Е	Aug-22 st @ Comp	Net Contingency Balance	Budget Summary Notes
ACMA Replacement	\$ 28,300,000	\$ 36,552,76	7 \$	36,552,767	\$	36,552,767		
AHS Title IX Compliance	\$ 2,000,000	\$ 3,453,43	3 \$	3,453,433	\$	3,453,433		Completed; Final Cost
Capital Center Improvements & Data Center	\$ 5,000,000	\$ 12,820,18	7 \$	12,820,187	\$	12,820,187		Completed; Final Cost
District-Wide ADA Compliance	\$ 2,000,000	\$ 1,523,77	7 \$	1,523,777	\$	1,523,777		Projects in Process; budget 52% complete
District-Wide Communication System	\$ 7,200,000	\$ 5,282,07	2 \$	5,282,072	\$	5,282,072		Completed; Final Cost
District-Wide Facility Repairs	\$ 98,000,000	\$ 121,506,35	0 \$	121,506,350	\$	121,506,350		
District-Wide HVAC Controls	\$ 800,000	\$ 800,00	0 \$	800,000	\$	800,000		Projects in Process; budget 33% complete
Domestic / Fire Line Separation	\$ 800,000	(Budget moved t Facilities Repair	)					
Five Oaks MS Renovation & Expansion	\$ 21,100,000			28,195,854	\$	28,195,854		
Green Energy Technology	\$ 5,000,000	(Budget Moved to Other Projects)	)					Scope completed via new schools and rebuilds
Hazeldale K-5 Replacement	\$ 24,600,000	\$ 31,504,98	2 \$	31,504,982	\$	31,504,982		Completed; Final Cost
IT Data Center @ Capital Center	\$ 2,900,000	(Budget Moved t CC Project)	)					Scope completed via Capital Center Improvements
Kitchen Improvements	\$ 800,000	\$ 977,12	0 \$	977,120	\$	977,120		Projects in Process; budget 80% complete
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000	\$ 7,772,65	9 \$	7,772,659	\$	7,772,659		Completed; Final Cost
Maintenance Facility Improvements Phase I	\$ 10,000,000	\$ 11,263,99	0 \$	11,263,990	\$	11,263,990		In Close-Out;
McKay ADA Improvements	\$ 400,000	\$ 634,54	0 \$	634,540	\$	634,540		Completed; Final Cost
New HS: Mountainside	\$ 109,000,000	\$ 184,135,29	4 \$	184,135,294	\$	184,135,294		In Close-Out;
New ES: Sato K5	\$ 25,000,000	\$ 38,097,64	2 \$	38,097,642	\$	38,097,642		Completed; Final Cost
New MS: Tumwater	\$ 51,600,000	\$ 61,691,09	6 \$	61,691,096	\$	61,691,096		Construction completed 2016;
Raleigh Hills K-8 Improvements	\$ 9,700,000	\$ 1,419,49	0 \$	1,419,490	\$	1,419,490		Completed; Final Cost
Raleigh Hills K-8 Conceptual Design	\$ -	\$ 1,000,00	0 \$	1,000,000	\$	1,000,000		
Raleigh Hills K-8 Improvements	\$ -	\$ 10,821,75	3 \$	10,821,753	\$	10,821,753		Funding Raleigh Hills Replacement with additional funds from 2022 Bond
Security Upgrades	\$ 10,000,000	\$ 18,458,53	0 \$	18,458,530	\$	18,458,530		Projects in Process; budget 96% complete
Seismic Upgrades	\$ 4,200,000	\$ 26,197,69	2 \$	26,197,692	\$	26,197,692		Projects in Process; budget 86% complete

Project List	riginal Budget Allocations	rised Approved urrent Budget		July-22 st @ Comp	Е	Aug-22 st @ Comp	Net Contingency Balance	Budget Summary Notes
SHS Title IX Compliance	\$ 2,000,000	\$ 4,285,317	\$	4,285,317	\$	4,285,317		Completed; Final Cost
Springville K-8 Improvements	\$ 2,000,000	\$ 510,016	\$	510,016	\$	510,016		Completed; Final Cost
Vose K-5 Replacement	\$ 24,800,000	\$ 33,846,280	\$	33,846,280	\$	33,846,280		Completed; Final Cost
William Walker K-5 Replacement	\$ 24,600,000	\$ 34,626,711	\$	34,626,711	\$	34,626,711		Completed; Final Cost
Added Projects	\$ -	\$ 12,491,010	\$	12,491,010	\$	12,491,010		Projects in Process; budget 65% complete
Program Contingency	\$ 45,400,000							
Program Inflation	\$ 52,800,000							
Pre-Bond Expenditure Reimbursements	\$ 1,000,000	\$ 998,828	\$	998,828	\$	998,828		Completed; Final Cost
Bond Management Costs	\$ 20,000,000	\$ 30,990,506	\$	30,990,506	\$	30,990,506		
Bond Issuance Costs	\$ 6,000,000	\$ 4,000,000	\$	4,000,000	\$	4,000,000		
Construction Subtotal	\$ 600,000,000	\$ 725,857,896	\$ 7	725,857,896	\$ 7	25,857,896	-	
Learning Technology	\$ 56,000,000	\$ 56,000,000	\$	56,000,000	\$	56,000,000		
Critical Equipment	\$ 24,000,000	\$ 24,000,000	\$	24,000,000	\$	24,000,000		
Tech & Equip Subtotal	\$ 80,000,000	\$ 80,000,000	\$	80,000,000	\$	80,000,000		
Grand Totals	\$ 680,000,000	\$ 805,857,896	\$ 8	805,857,896	\$ 8	05,857,896	\$ -	
Added Funding to Bond Program								
Bond Premium (First Bond Sale)	\$ 63,295,961							
Bond Premium (Second Bond Sale)	\$ 30,270,107							
Interest Earnings (First Bond Sale)	\$ 5,340,214							
Interest Earnings (Second Bond Sale)	\$ 13,236,261							
Other Additional Funding (see Tab)	\$ 16,039,545							
Grand Total Added Funding	\$ 128,182,088							
GRAND TOTAL 2014 BOND FUNDING	\$ 808,182,088							Total Funding did not change.
Program Reserve		\$ 2,324,191						-
Program Reserve + Project Contingencies							\$ 2,324,191	PR EAC + Contingencies reduced by \$105

Source	Funding	Assigned to Projects	Assigned to Program Reser		Budget Summary Notes
Remaining 2006 Bond Savings	\$ 576,615	Mountainside HS	\$	-	
Capital Center Rent Revenue Balance	\$ 433,385	Mountainside HS	\$	-	
Construction Excise Tax Revenue	\$ 1,130,655	Capital Center	\$	-	
Construction Excise Tax Revenue forecasted to 2021	\$ 5,021,577			\$5,021,577	
THPRD reimb.	\$ 449,783		\$	449,783	
SB 1149 reimb.	\$ 3,264,390	District-wide Repairs	\$	248,828	
ETO reimb.	\$ 1,635,632	District-wide Repairs	\$	1,448,553	
Facility grants	\$ 3,027,507		\$	3,027,507	
Sato: TVWD Reimbursement	\$ 500,000	Sato K-5	\$	-	
TOTAL	\$16,039,545			\$10,196,248	

Added Projects	Approved by & Date	Original Budget	Revised Approved Current Budget	July-22 Est @ Comp	Aug-22 Est @ Comp		Budget Summary Notes
						<u> </u>	
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$ 99,368	\$ 99,368	\$ 99,368		Completed; Final Cost
Portable Relocations 2014	Sr LT 5/20/14	\$ 17,956,364	\$ 591,685	\$ 591,685	\$ 591,685		Completed; Final Cost
Portable Relocations 2015	Sr LT 3/2015		\$ 294,257	\$ 294,257	\$ 294,257		Completed; Final Cost
Title IX Projects - Group II	Sr LT 3/2015		\$ 1,030,697	\$ 1,030,697	\$ 1,030,697		Completed; Final Cost
Classroom Door Locks	SB 6/18/18		\$ 2,179,293	\$ 2,179,293	\$ 2,179,293		Budget 85% complete; phase 2 work ongoing
Security Upgrades: Classroom Walls	SB 6/15/20		\$ 2,045,710	\$ 2,045,710	\$ 2,045,710		
Security Upgrades: Paging	SB 6/15/20		\$ 500,000	\$ 500,000	\$ 500,000		
Security Upgrades: Site Fencing	1635632.45		\$ 1,700,000	\$ 1,700,000	\$ 1,700,000		
Vose Classroom Addition	SB 6/21/21		\$ 3,900,000	\$ 3,900,000	\$ 3,900,000	\$ - 0%	Transferred \$150K to Sato Classroom
Sato Classroom Addition	SB 2/28/22		\$ 150,000	\$ 150,000	\$ 150,000		Design approved at 2/28/22 SB Meeting.
Added Projects Total		\$ 17,956,364	\$ 12,491,010	\$ 12,491,010			

Projects in Close-out         \$ 6,883,538 \$ 21,655,377 \$ 21,655,	Aug-22 Est @ Comp Net Contingency Balance	nce Budget Summary Notes
Projects in Close-out  \$ 6.883,538 \$ 21,655,377 \$ 21,655,		
2022 Repipes	\$ 59,818,969	Completed; Final Cost
2021 Roof Replacements \$ 1,972,000 \$ 5,100,797 \$ 5,100,797 \$ 5,10 Hiteon HVAC Controls Upgrade \$ 200,000 \$ 593,783 \$ 593,783 \$ 55 Raleigh Park Sewer \$ 47,000 \$ 100,000 \$ 100,000 \$ 10 ISB HVAC & Roof \$ 864,000 \$ 2,505,406 \$ 2,326,733 \$ 2,50 District-Wide Fire Alarm Resiliency \$ 1,303,000 \$ 2,474,120 \$ 2,474,120 \$ 2,47 2022 Roof Replacements 1 (NR, McK, Findley) \$ 1,380,000 \$ 3,323,273 \$ 3,323,273 \$ 3,32 2022 Roof Replacements 2 (Fir Grove, Grwy) \$ 277,000 \$ 2,665,152 \$ 2,665,152 \$ 2,665,152 \$ 2,665,152 \$ 2,665,152 \$ 2,665,152 \$ 2,264 2022 HVAC Upgrades 1 (EH, Kinnaman, McK) \$ 882,000 \$ 114,080 \$ 114,080 \$ 11 2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) \$ 1,712,000 \$ 97,600 \$ 1,712,000 \$ \$ Five Oaks Roof \$ - \$ 416,000 \$ 416,000 \$ 41 New Schools Post-Warranty Fund \$ - \$ 650,000 \$ 650,000 \$ 65 Maint Dept Repair & Improvement & Other Projects* \$ 9,068,708 \$ 11,753,115 \$ 10,439,322 \$ 11,80 Repair Program Balance Available \$ 44,688,049 \$ 9,081,421 \$ 9,014,394 \$ 8,60 Repair Program Budget (Less Transfers In/Out) \$ 98,000,000 \$ 121,506,350 \$ 12	\$ 21,655,377 \$ 545,097	.6%
Hiteon HVAC Controls Upgrade	\$ 1,500,000 \$ 150,000 11.	1.1%
Raleigh Park Sewer \$ 47,000 \$ 100,00	\$ 5,100,797 \$ 124,566 2.8	.5%
ISB HVAC & Roof	\$ 593,783 \$ - 0.0	.0%
District-Wide Fire Alarm Resiliency \$ 1,303,000 \$ 2,474,120 \$ 2,47	\$ 100,000 \$ 10,650	1.9%
2022 Roof Replacements 1 (NR, McK, Findley) \$ 1,380,000 \$ 3,323,273 \$ 3,323,273 \$ 3,32  2022 Roof Replacements 2 (Fir Grove, Grwy) \$ 277,000 \$ 2,665,152 \$ 2,665,152 \$ 2,66  2022 HVAC Upgrades 1 (EH, Kinnaman, McK) \$ 882,000 \$ 114,080 \$ 114,080 \$ 11  2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) \$ 1,712,000 \$ 97,600 \$ 1,712,000 \$ 5  Five Oaks Roof \$ - \$ 416,000 \$ 416,000 \$ 47  New Schools Post-Warranty Fund \$ - \$ 650,000 \$ 650,000 \$ 650  Maint Dept Repair & Improvement & Other Projects* \$ 9,068,708 \$ 11,753,115 \$ 10,439,322 \$ 11,80  Repair Projects Total \$ 53,311,951 \$ 112,822,579 \$ 112,491,956 \$ 112,82  Repair Program Balance Available \$ 44,688,049 \$ 9,081,421 \$ 9,014,394 \$ 8,66  Repair Program Badget (Less Transfers In/Out) \$ 98,000,000 \$ 121,506,350 \$ 121,506,350 \$ 121,506  Budget and Est @ Comp. will increase each month as additional Maintenance Dept. managed Repair Projects are scheduled.  Transfer Tracking	\$ 2,505,406	.0%
2022 Roof Replacements 2 (Fir Grove, Grwy) \$ 277,000 \$ 2,665,152 \$ 2,665,152 \$ 2,665 2022 HVAC Upgrades 1 (EH, Kinnaman, McK) \$ 882,000 \$ 114,080 \$ 114,080 \$ 11 2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) \$ 1,712,000 \$ 97,600 \$ 1,712,000 \$ 9 Five Oaks Roof \$ - \$ 416,000 \$ 416,000 \$ 47 New Schools Post-Warranty Fund \$ - \$ 650,000 \$ 650,000 \$ 65 Maint Dept Repair & Improvement & Other Projects* \$ 9,068,708 \$ 11,753,115 \$ 10,439,322 \$ 11,80  Repair Projects Total \$ 53,311,951 \$ 112,822,579 \$ 112,491,956 \$ 112,82 Repair Program Balance Available \$ 44,688,049 \$ 9,081,421 \$ 9,014,394 \$ 8,68 Repair Program EAC Balance \$ - \$ -  Repair Program Budget (Less Transfers In/Out) \$ 98,000,000 \$ 121,506,350	\$ 2,474,120 \$ - 0.0	.0%
2022 HVAC Upgrades 1 (EH, Kinnaman, McK) \$ 882,000 \$ 114,080 \$ 114,080 \$ 11  2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) \$ 1,712,000 \$ 97,600 \$ 1,712,000 \$ 9  Five Oaks Roof \$ - \$ 416,000 \$ 416,000 \$ 41  New Schools Post-Warranty Fund \$ - \$ 650,000 \$ 650,000 \$ 65  Maint Dept Repair & Improvement & Other Projects* \$ 9,068,708 \$ 11,753,115 \$ 10,439,322 \$ 11,80  Repair Projects Total \$ 53,311,951 \$ 112,822,579 \$ 112,491,956 \$ 112,82  Repair Program Balance Available \$ 44,688,049 \$ 9,081,421 \$ 9,014,394 \$ 8,66  Repair Program EAC Balance \$ - \$ -  Repair Program Budget (Less Transfers In/Out) \$ 98,000,000 \$ 121,506,350 \$ 121,506,350 \$ 121,506  "Budget and Est @ Comp. will increase each month as additional Maintenance Dept. managed Repair Projects are scheduled.  Transfer Tracking	\$ 3,323,273 \$ 307,600 10.	These will be 2023 roof projects.
2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) \$ 1,712,000 \$ 97,600 \$ 1,712,000 \$ 5	\$ 2,665,152 \$ 58,576	.2%
Five Oaks Roof	\$ 114,080 0.0	.0% split funded with ESSER
New Schools Post-Warranty Fund	\$ 97,600	.0% Balance moved to ESSER
Maint Dept Repair & Improvement & Other Projects*	\$ 416,000 \$ 29,000 7.8	.5%
Repair Projects Total   \$ 53,311,951   \$ 112,822,579   \$ 112,491,956   \$ 112,822	\$ 650,000	
Repair Program Balance Available   \$ 44,688,049   \$ 9,081,421   \$ 9,014,394   \$ 8,68	\$ 11,808,022	
Repair Program EAC Balance   \$ - \$ -   \$   -   \$	\$ 112,822,579	
Repair Program Budget (Less Transfers In/Out)   \$ 98,000,000   \$ 121,506,350	\$ 8,683,771	
*Budget and Est @ Comp. will increase each month as additional Maintenance Dept. managed Repair Projects are scheduled.  Transfer Tracking		
Transfer Tracking	\$ 121,506,350	
Initial Budget		
Previous Transfers         \$ 22,091,701           SB 1149 Reimbursements         \$ 3,015,562           ETO Reimbursements         \$ 187,079           Funds transferred to Seismic- Bethany ES         \$ (2,230,000)           Funds transferred to Added Projects - Classroom Door Locks         \$ (179,293)           Additional Funding - Elmonica Repipe - Approved 6.21.2021         \$ 500,000           Funds transferred to Added Projects - Classroom Walls         \$ (45,710)           Funds transferred from Five Oaks         \$ 150,000           Funds transferred to Seismic- West TV ES         \$ (460,827)           Transfer from Seismic for Roof Repl - Group 1         \$ 247,273		
SB 1149 Reimbursements       \$ 3,015,562         ETO Reimbursements       \$ 187,079         Funds transferred to Seismic- Bethany ES       \$ (2,230,000)         Funds transferred to Added Projects - Classroom Door Locks       \$ (179,293)         Additional Funding - Elmonica Repipe - Approved 6.21.2021       \$ 500,000         Funds transferred to Added Projects - Classroom Walls       \$ (45,710)         Funds transferred from Five Oaks       \$ 150,000         Funds transferred to Seismic- West TV ES       \$ (460,827)         Transfer from Seismic for Roof Repl - Group 1       \$ 247,273		
ETO Reimbursements         \$ 187,079           Funds transferred to Seismic- Bethany ES         \$ (2,230,000)           Funds transferred to Added Projects - Classroom Door Locks         \$ (179,293)           Additional Funding - Elmonica Repipe - Approved 6.21.2021         \$ 500,000           Funds transferred to Added Projects - Classroom Walls         \$ (45,710)           Funds transferred from Five Oaks         \$ 150,000           Funds transferred to Seismic- West TV ES         \$ (460,827)           Transfer from Seismic for Roof Repl - Group 1         \$ 247,273		
Funds transferred to Seismic- Bethany ES       \$ (2,230,000)         Funds transferred to Added Projects - Classroom Door Locks       \$ (179,293)         Additional Funding - Elmonica Repipe - Approved 6.21.2021       \$ 500,000         Funds transferred to Added Projects - Classroom Walls       \$ (45,710)         Funds transferred from Five Oaks       \$ 150,000         Funds transferred to Seismic- West TV ES       \$ (460,827)         Transfer from Seismic for Roof Repl - Group 1       \$ 247,273	+ + + - +	
Funds transferred to Added Projects - Classroom Door Locks       \$ (179,293)         Additional Funding - Elmonica Repipe - Approved 6.21.2021       \$ 500,000         Funds transferred to Added Projects - Classroom Walls       \$ (45,710)         Funds transferred from Five Oaks       \$ 150,000         Funds transferred to Seismic- West TV ES       \$ (460,827)         Transfer from Seismic for Roof Repl - Group 1       \$ 247,273	+	
Additional Funding - Elmonica Repipe - Approved 6.21.2021       \$ 500,000         Funds transferred to Added Projects - Classroom Walls       \$ (45,710)         Funds transferred from Five Oaks       \$ 150,000         Funds transferred to Seismic- West TV ES       \$ (460,827)         Transfer from Seismic for Roof Repl - Group 1       \$ 247,273	+ + + - +	-
Funds transferred to Added Projects - Classroom Walls       \$ (45,710)         Funds transferred from Five Oaks       \$ 150,000         Funds transferred to Seismic- West TV ES       \$ (460,827)         Transfer from Seismic for Roof Repl - Group 1       \$ 247,273	+ + + + + + + + + + + + + + + + + + + +	-
Funds transferred from Five Oaks         \$ 150,000           Funds transferred to Seismic- West TV ES         \$ (460,827)           Transfer from Seismic for Roof Repl - Group 1         \$ 247,273	+ + + + + + + + + + + + + + + + + + + +	
Funds transferred to Seismic- West TV ES \$ (460,827)  Transfer from Seismic for Roof Repl - Group 1 \$ 247,273		
Transfer from Seismic for Roof Repl - Group 1 \$ 247,273	+ + + + + + + + + + + + + + + + + + + +	
	+ + + + + + + + + + + + + + + + + + + +	
Balance \$ 121,506,350		

Seismic Projects	Original Budget		Revised Approved Current Budget			Aug-22 Est @ Comp		Net Contingency Balance	Budget Summary Notes	
A/E Scoping/Surveys	\$	-	\$ 222,058	\$	222,058	\$	222,058		Completed; Final Cost	
Aloha HS	\$	1,732,898	\$ 17,956,364	\$	17,956,364	\$	17,956,364		Completed; Final Cost	
Beaver Acres ES	\$	1,714,444	\$ 5,926,866	\$	5,926,866	\$	5,926,866		Completed: Final Cost	
Beaverton HS	\$	246,184	(Budget Transferred						Scope completed via BHS Gym Ceiling project	
Cedar Mill ES	\$	144,771	to Seismic Program) (Budget Moved to							
	φ	144,771	Facility Repairs)						Scope completed via Cedar Mill Roof & HVAC project	
Cooper Mt. ES	\$	361,703	\$ 2,729,215	\$	2,729,215	\$	2,729,215	0.0%	In Close-Out;	
Bethany ES	\$	-	\$ 4,930,811	\$	4,930,811	\$	4,930,811	0.0%		
Seismic Red Zones	\$	1,635,632	\$ 160,300	\$	160,300	\$	160,300			
2022 SRGP Planning	\$	-	\$ 100,000	\$	100,000	\$	100,000			
West TV Seismic (Gym)	\$	-	\$ 597,827	\$	597,827	\$	597,827	0.0%		
Seismic Red Zones (Rock Creek/SHS)	\$	-	\$ 239,700	\$	239,700	\$	239,700		Project is now under contract, bid results increase budget from seismic funding hold by about \$30K.	
Seismic Funding Hold	\$	-	\$ 597,837	\$	597,837	\$	597,837		Tantaing nota by about 4001.	
(Projects Financially Complete)										
Seismic Projects Total	\$	5,835,632	\$ 33,460,978	\$	33,460,978	\$	33,460,978			
TAPS Seismic Grant	\$	-	\$ (22,545	) \$	(22,545)	\$	(22,545)			
AHS Seismic Rehabilitation Grant	\$	-	\$ (2,500,000	) \$	(2,500,000)	\$	(2,500,000)			
Beaver Acres Seismic Rehabilitation Grant	\$	_	\$ (2,500,000	· ) \$	(2,500,000)	\$	(2,500,000)			
Cooper Mnt Seismic Rehabilitation Grant	\$		• • • • • • • • • • • • • • • • • • • •		(2,240,741)		(2,240,741)			
Seismic Program Bond Cost Balance	\$	4,200,000			26,197,692	1	26,197,692			
Seismic Program Less Transfers In/Out	\$	26,197,692								
Colonia i rogram 2000 i anolo	Ť	20,101,002								
Transfer Tracking										
Initial Budget	\$	4,200,000								
Program Escalation	\$	1,006,740								
AHS Roofing - From Facility Repairs	\$	575,193								
Beaver Acres Roofing - From Facility Repairs  AHS Roofing - Balance From Facility Repairs	\$	1,138,000 3,477,807		-						
Program Reserve - Approved by School Board 6.18.18	\$	5,450,000		-						
Transfer to Facility Repairs - Cedar Mill	\$	(166,052)								
Cooper Mnt Roofing - From Facility Repairs	\$	128,000								
Program Reserve - Approved by School Board 10.28.19	\$	6,849,950	-							
Beaver Acres Windows - From Facility Repairs	\$	605,000		_						
Beaver Acres Re-pipe - From Facility Repairs	\$	489,500								
Bethany Roof and HVAC Seismic Transfer	\$	2,230,000								
West TV Seismic (Gym) Transfer Transfer to McKinley Roofing (2022 Roof Phase 1)	\$	460,827 (247,273)								
Balance	,	26,197,692								
Dalatice	Ψ	20,107,002						l l	Page 11	

