


Bond Program Status Report

Through January 2020

2014 Bond Program Executive Summary January 2020

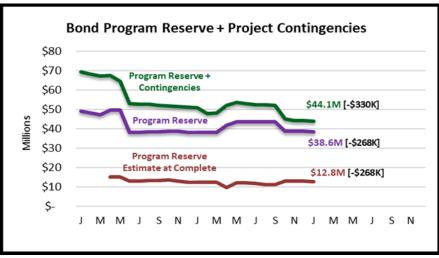

Bond Program Reserve = Funding available to the Bond Program but not yet allocated to a project Project Contingencies = Funding contained within an approved project budget

Bond Program Funding Total		\$ 807,115,557
Revised Approved Current Budget	-	\$ 768,544,112
Bond Program Reserve		\$ 38,571,445
Bond Program Reserve		\$ 38,571,445
Net Contingency Balance	+	\$ 5,517,948
Bond Program Reserve + Contingencies		\$ 44,089,393
Bond Program Funding Total		\$ 807,115,557
Program Estimate at Complete (EAC)	-	\$ 794,344,112
Projected Program Reserve Estimate at Complete		\$ 12,771,445

Budget Perspective

This month the overall Program Reserve decreased by -\$268K, while the Reserve + Project Contingencies decreased by -\$330K. All projects remain within their current approved budgets. Primary cost events were:

- On January 9th, 2020, the fire alarm and intrusion system at Aloha High School failed. In order to replace the system as quickly as possible an emergency was declared and \$150K was transferred from the Program Reserve into the District-Wide Facility Repairs, as approved by Chief Facilities Officer Josh Gamez in accordance with the Cost Management and Control Plan. A vendor is already under contract for the replacement, with full time building monitoring and fire watch in place until the work is complete.
- Security Upgrades budget has been increased by \$150K due to the need for additional cameras at the high schools, as approved by Chief Facilities Officer Josh Gamez in accordance with the Cost Management and Control Plan.
- Whitford HVAC and Roof's budget increased by \$1.9M based on the GMP cost proposal, which was in line with our estimates.
- Additional funding for the Bond increased by \$251K. \$32K was due to an ETO reimbursement from William Walker, and has been assigned to the Program Reserve. \$219K was due to SB1149 reimbursements from Merlo Station HVAC and Roof, and has been assigned to the District-Wide Facility Repair project.

Schedule Perspective


- · ACMA has completed installation of steel and trusses. Deck work is well along, and completed in several areas.
- Five Oaks has turned over use of the new vestibule to staff. Punch list walk and turnover for Phase 5 (west classroom wing) should be taking place through February. Demo for Phase 6 (special education wing) is now continuing at full time. Staff continue to work with the contractor on mitigating and incorporating cost events, but it is likely a budget increase will be needed in order to execute Phase 7.
- Security Upgrades has completed camera installation at Westview and is starting at Southridge. Group 3 perimeter hardening is completed and in punch. Negotiations for the final group (4) of perimeter hardening ongoing.

Challenges and Opportunities

- Market Conditions: cost overruns on specific trades (such as HVAC); few prequalified bidders on Beaver Acres Seismic (two); bidding for most major Summer 2020 projects should be complete through March
- Oregon CAT (Corporate Activity Tax): went into effect on January 1, 2020; already seeing contractors working the tax (0.57%) into bids; BSD has taken the stance that as a tax exempt agency vendors cannot pass through the burden
- District-Wide Facility Repairs: projecting \$5.2M in remaining budget, before all Summer 2020 projects bid; over \$30M of work remaining; budget increase needed to complete promised Bond work

School Bond Program 2020 Activity Map



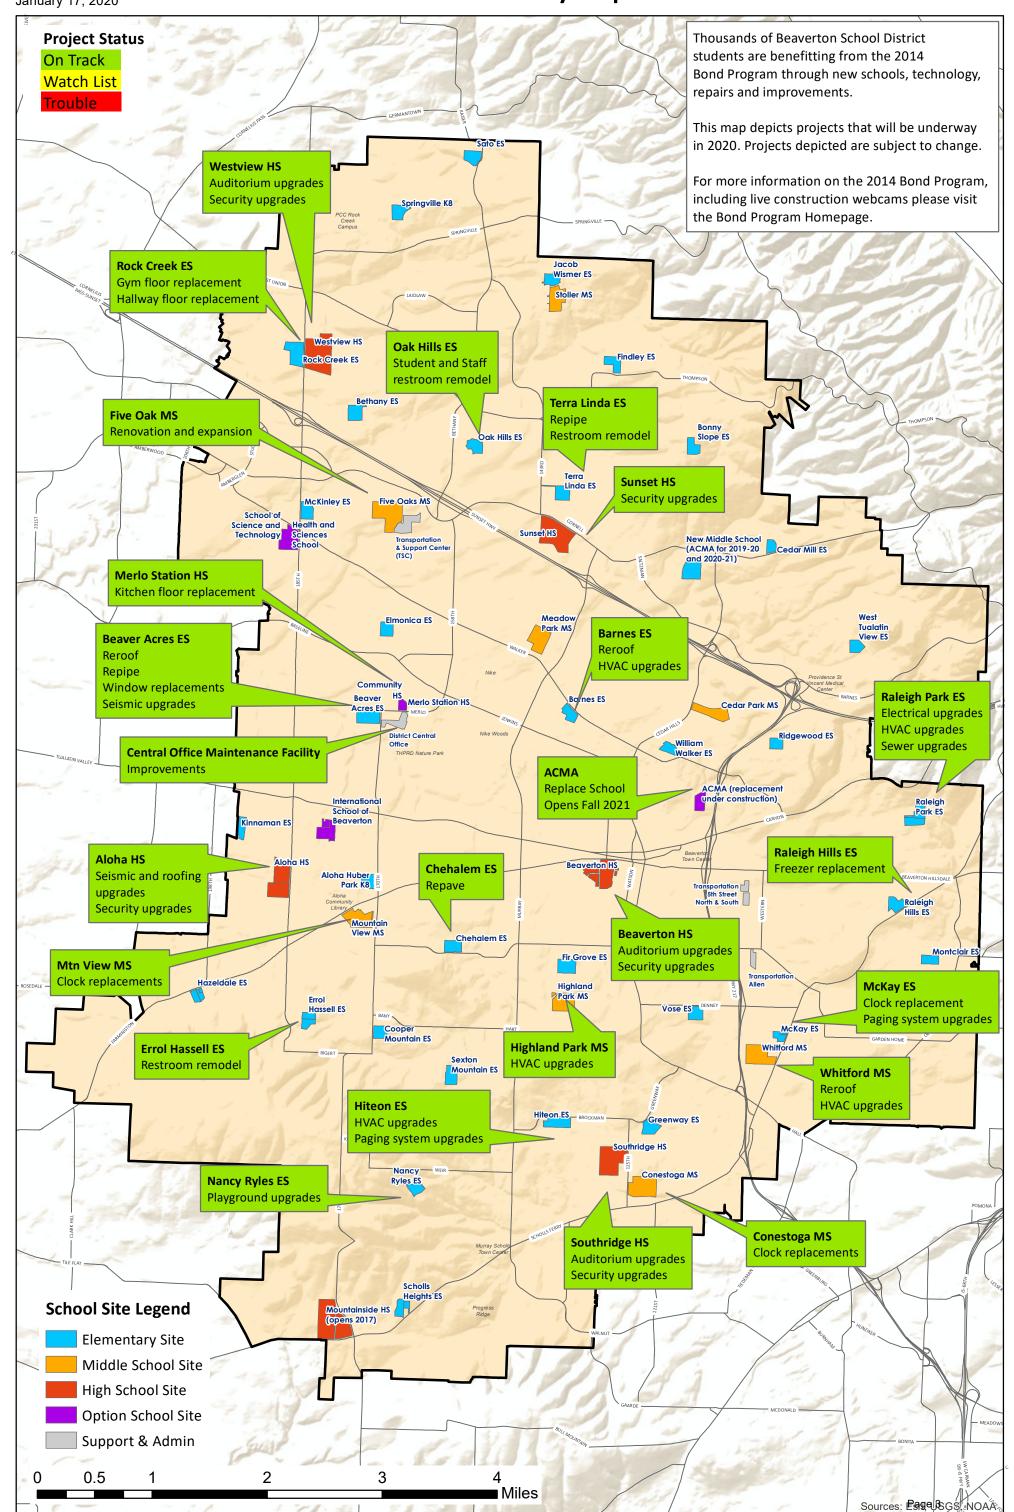

2014 Bond Program Scorecard January 2020

Performance Key

Green = On Track

Yellow = Watchlist

Red = Trouble

Gray = Milestone Complete

(Date) = Target


Date = Actual

N/A = Not Applicable


TYTE TOUT Applicable	I								
Current Performance Metrics	ACMA Replacement	Five Oaks Renovation	Maintenance Facility	Aloha High School Seismic & Roofing	Highland Park & Whitford HVAC	Beaver Acres Seismic & Renovation	Raleigh Park HVAC & Electrical	Barnes Roof & HVAC	Terra Linda Repipe
Overall Budget Performance	On Track	Trouble	On Track	On Track	On Track	On Track	Watchlist	On Track	On Track
Budget Percent Complete	27.00%	72.00%	80.00%	27.00%	4.00%	2.00%	3.00%	4.00%	5.00%
Overall Schedule Performance	On Track	On Track	Watchlist	On Track	On Track	On Track	On Track	On Track	On Track
Schedule Percent Complete	38.00%	72.00%	60.00%	35.00%	0.00%	0.00%	0.00%	0.00%	0.00%
						1	1		
Schedule Milestones	ACMA Renovation	Five Oaks Renovation	Maintenance Facility	Aloha High School Seismic & Roofing	Highland Park & Whitford HVAC	Beaver Acres Seismic & Renovation	Raleigh Park HVAC & Electrical	Barnes Roof & HVAC	Terra Linda Repipe
Design Team Contracted	5-2016	6-2016	6-2016	9-2018	9-2018	8-2019	8-2019	8-2019	7-2019
Design - Schematic Design	3-2018	10-2017	3-2017	11-2018	10-2018	10-2019	12-2019	10-2019	9-2019
Design - Design Development	8-2018	11-2017	10-2018	1-2019	11-2018	11-2019	1-2020	11-2019	12-2019
Design - Construction Documents	2-2019	5-2018	1-2019	3-2019	3-2019	1-2020	(2-2020)	1-2020	1-2020
Permitting - Land Use	1-2019	3-2018	1-2019	N/A	N/A	N/A	N/A	N/A	N/A
Permitting - Site Development	5-2019	7-2018	4-2019	N/A	N/A	N/A	N/A	N/A	N/A
Permitting - Building	7-2019	6-2018	4-2019	11-2019	(5-2020)	(5-2020)	(6-2020)	(5-2020)	(6-2020)
Construction - Contract Award	5-2019	9-2017	7-2017	2-2019	8-2019	(3-2020)	(4-2020)	(4-2020)	(3-2020)
Construction - Start	7-2019	6-2018	3-2019	6-2019	(6-2020)	(6-2020)	(6-2020)	(6-2020)	(6-2020)
Construction - Finish	(8-2021)	(8-2020)	(8-2020)	(8-2020)	(9-2020)	(8-2020)	(8-2020)	(8-2020)	(9-2020)
Owner Activities - FF&E Ordered	(2-2021)	3-2019	N/A	N/A	N/A	(6-2020)	N/A	N/A	N/A
Owner Activities - FF&E Delivered	(5-2021)	(8-2020)	N/A	N/A	N/A	(8-2020)	N/A	N/A	N/A
Owner Activities - Occupancy	(6-2021)	(8-2020)	(8-2020)	(8-2020)	(9-2020)	(8-2020)	(9-2020)	(9-2020)	(9-2020)
Project Complete (Month - Year)	(8-2021)	(8-2020)	(8-2020)	(8-2020)	(8-2020)	(8-2020)	(9-2020)	(9-2020)	(9-2020)
Equity Goals									
Participation	Target %	Current %	Change %						
MWSDVE - Consultants	10.0%	15.0%	0.10%						
MWSDVE - Contractors	10.0%	13.2%	-0.20%						
Apprenticeship	10.0%	20.0%	No change						

2014 Construction Bond Program

Equity Performance January 2020 Report

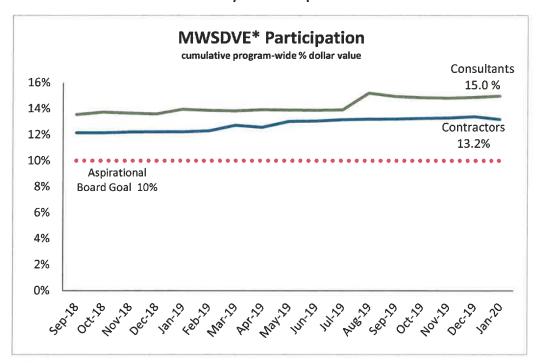

^{*}Minority, Women and Service Disabled Veteran Owned Enterprises

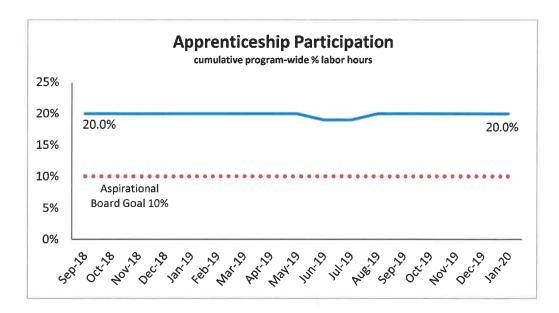

2014 Bond Program Financial Status Report Financial Summary

Project List	jinal Budget Ilocations	sed Approved rrent Budget		ec-19 @ Comp	ı	Jan-20 Est @ Comp	Net Contingen	ncy Balance	Budget Summary Notes
ACMA Replacement	\$ 28,300,000	\$ 37,570,155	\$	37,570,155	\$	37,570,155	\$ 3,066,999	8.9%	Current contingency decreased by (\$73K) due to design clarifications
AHS Title IX Compliance	\$ 2,000,000	\$ 3,453,433	\$	3,453,433	\$	3,453,433			Completed; Final Cost
Capital Center Improvements & Data Center	\$ 5,000,000	\$ 12,820,187	\$	12,820,187	\$	12,820,187			Completed; Final Cost
District-Wide ADA Compliance	\$ 2,000,000	\$ 2,000,000	\$	2,000,000	\$	2,000,000			Projects in Process; budget 15% complete
District-Wide Communication System	\$ 7,200,000	\$ 5,282,072	\$	5,282,072	\$	5,282,072			Completed; Final Cost
District-Wide Facility Repairs	\$ 98,000,000	\$ 94,428,390	\$ 1	19,858,926	\$	120,228,390			Current budget increased by +369K . \$219K due to additional SB 1149 revenue; \$150K for the AHS Fire Alarm Replacement, as approved by Chief Faculties Officer Josh Gamez.
District-Wide HVAC Controls	\$ 800,000	\$ 800,000	\$	800,000	\$	800,000			Projects in Process; budget 33% complete
Domestic / Fire Line Separation	\$ 800,000	\$ 977,120	\$	977,120	\$	977,120			Budget 0% complete
Five Oaks MS Renovation & Expansion	\$ 21,100,000	\$ 28,001,419	\$	28,001,419	\$	28,001,419	\$ 2,795	0.0%	
Green Energy Technology	\$ 5,000,000	dget Moved to her Projects)							Scope completed via new schools and rebuilds
Hazeldale K-5 Replacement	\$ 24,600,000	\$ 31,756,091	\$	31,756,091	\$	31,756,091	\$ 120,024		In Close-Out; Construction Completed 2018
IT Data Center @ Capital Center	\$ 2,900,000	dget Moved to CC Project)							Scope completed via Capital Center Improvements
Kitchen Improvements	\$ 800,000	\$ 977,120	\$	977,120	\$	977,120			Projects in Process; budget 17% complete
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000	\$ 7,800,000	\$	7,800,000	\$	7,800,000			In Close-Out; Purchase completed 2019
Maintenance Facility Improvements Phase I	\$ 10,000,000	\$ 11,263,990	\$	11,263,990	\$	11,263,990	\$ 179,948	1.6%	
McKay ADA Improvements	\$ 400,000	\$ 634,540	\$	634,540	\$	634,540			Completed; Final Cost
New HS: Mountainside	\$ 109,000,000	\$ 184,135,294	\$ 1	84,135,294	\$	184,135,294	\$ 365,676		In Close-Out; Construction Completed 2017
New ES: Sato K5	\$ 25,000,000	\$ 38,175,000	\$	38,175,000	\$	38,175,000	\$ 83,666		In Close-Out; Construction Completed 2017
New MS @ Timberland	\$ 51,600,000	\$ 61,371,096	\$	61,371,096	\$	61,371,096	\$ 261,073		Construction completed 2016; remaining budget reserved for final outfitting
Raleigh Hills K-8 Improvements	\$ 9,700,000	\$ 1,419,490	\$	1,419,490	\$	1,419,490			Completed; Final Cost
Raleigh Hills K-8 Improvements (Funding Hold)	\$ -	\$ 11,821,753	\$	11,821,753	\$	11,821,753			
Security Upgrades	\$ 10,000,000	\$ 14,771,670	\$	14,621,670	\$	14,771,670			Current budget increased by +\$150K due to the need for additional cameras at the high schools, as approved by Chief Faculties Officer Josh Gamez.
Seismic Upgrades	\$ 4,200,000	\$ 23,754,138	\$	23,754,138	\$	23,754,138			

2014 Bond Program Financial Status Report Financial Summary

Project List		ginal Budget Ilocations		vised Approved urrent Budget		Dec-19 Est @ Comp		Jan-20 Est @ Comp	Net Continger	ncy Balance	Budget Summary Notes
SHS Title IX Compliance	\$	2,000,000	\$	4,285,317	\$	4,285,317	\$	4,285,317			Completed; Final Cost
Springville K-8 Improvements	\$	2,000,000	\$	510,016	\$	510,016	\$	510,016			Completed; Final Cost
Vose K-5 Replacement	\$	24,800,000	\$	33,846,280	\$	33,846,280	\$	33,846,280			Completed; Final Cost
William Walker K-5 Replacement	\$	24,600,000	\$	36,684,200	\$	36,684,200	\$	36,684,200	\$ 1,437,767	4.1%	
Added Projects	\$	-	\$	4,016,007	\$	4,016,007	\$	4,016,007			
Program Contingency	\$	45,400,000									
Program Inflation	\$	52,800,000									
Pre-Bond Expenditure Reimbursements	\$	1,000,000	\$	998,828	\$	998,828	\$	998,828			Completed; Final Cost
Bond Management Costs	\$	20,000,000	\$	30,990,506	\$	30,990,506	\$	30,990,506			
Bond Issuance Costs	\$	6,000,000	\$	4,000,000	\$	4,000,000	\$	4,000,000			
Construction Subtotal	\$	600,000,000	\$	688,544,112	\$	713,824,648	\$	714,344,112	\$ 5,517,948		
Learning Technology	\$	56,000,000	\$	56,000,000	\$	56,000,000	\$	56,000,000			
Critical Equipment	\$	24,000,000	\$	24,000,000	\$	24,000,000	\$	24,000,000			
Tech & Equip Subtotal	\$	80,000,000	\$	80,000,000	\$	80,000,000	\$	80,000,000			
Grand Totals	\$	680,000,000	\$	768,544,112	\$	793,824,648	\$	794,344,112	\$ 5,517,948		Contingency Balance change of (\$63K)
Added Funding to Bond Program											
Bond Premium (First Bond Sale)	\$	63,295,961									
Bond Premium (Second Bond Sale)	\$	30,270,107									
Interest Earnings (First Bond Sale)	\$	5,340,214									
Interest Earnings (Second Bond Sale)	\$	13,236,261									
Other Additional Funding (see Tab)	\$	14,973,014									
Grand Total Added Funding	\$ 1	27,115,557									
GRAND TOTAL 2014 BOND FUNDING	S 8	307,115,557									Total Funding increased by +\$251K
Program Reserve		,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	\$	38,571,445	\$	13,038,970	\$	12,771,445			Program Reserve change of (\$268K)
Program Reserve + Project Contingencies			-	,,	*	-,,	-	_,,		\$ 44,089,393	Change of (\$330K)

2014 Bond Program Financial Status Report Additional Funding Allocations to Bond Program

Source	Funding	Assigned to Projects	ssigned to gram Reserve	Budget Summary Notes
Remaining 2006 Bond Savings	\$ 576,615	Mountainside HS	\$ -	
Capital Center Rent Revenue Balance	\$ 433,385	Mountainside HS	\$ -	
Construction Excise Tax Revenue	\$ 1,130,655	Capital Center	\$ -	
Construction Excise Tax Revenue forecasted to 2021	\$ 5,021,577	·	\$5,021,577	
THPRD reimb.	\$ 449,783		\$ 449,783	
SB 1149 reimb.	\$ 2,623,511	District-wide Repairs	\$	Reimbursements increased by +\$219K (Merlo Station Roof & HVAC)
ETO reimb.	\$ 1,209,981	District-wide Repairs	\$ 7 760 370	Reimbursements increased by +\$32K (William Walker)
Facility grants	\$ 3,027,507		\$ 3,027,507	
Sato: TVWD Reimbursement	\$ 500,000	Sato K-5	\$ -	
TOTAL	\$14,973,014		\$9,659,187	

2014 Bond Program Financial Status Report Added Projects


Added Projects	Approved by & Date	Original Budget	Revised Approved Current Budget		Dec-19 Est @ Comp	E	Jan-20 st @ Comp	Net Contingency Balance	Budget Summary Notes
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$ 99,368	3 \$	99,368	\$	99,368	\$ -	Completed; Final Cost
Portable Relocations 2014	Sr LT 5/20/14		\$ 591,685	5 \$	591,685	\$	591,685	\$ -	Completed; Final Cost
Portable Relocations 2015	Sr LT 3/2015		\$ 294,257	7 \$	294,257	\$	294,257	\$ -	Completed; Final Cost
Title IX Projects - Group II	Sr LT 3/2015		\$ 1,030,697	7 \$	1,030,697	\$	1,030,697	\$ -	Completed; Final Cost
Classroom Door Locks	SB 6/18/18		\$ 2,000,000	\$	2,000,000	\$	2,000,000	\$ -	Budget 54% complete; phase 2 surveys ongoing
Added Projects Total		e	¢ 4.046.00	, .	4 046 007	•	4 046 007		
Added Projects Total		\$ -	\$ 4,016,007	* *	4,016,007	Þ	4,016,007		

2014 Bond Program Financial Status Report District-Wide Repair Projects

"The \$98M"

Project	Initi	al Budget		sed Approved rent Budget	E	Dec-19 st @ Comp	E	Jan-20 st @ Comp	Net Contingency	Balance	Budget Summary Notes
Completed Projects	\$	23,852,331	\$	49,988,186	\$	43,334,804	\$	49,988,187			Completed; Final Cost
WHS Roof Replacement Phase I & 2	\$	2,055,558	\$	4,177,890	\$	4,476,673	\$	4,177,890	Completed; Fina	I Cost	Project financially closed
Highland Park Roof Replacement	\$	808,000	\$	2,475,493	\$	2,500,000	\$	2,475,493	Completed; Fina	I Cost	Project financially closed
Projects in Close-out	\$	2,281,574	\$	8,003,223	\$	14,979,896	\$	8,003,223	\$ 267,606	2.6%	
District-Wide Auditorium Upgrades	\$	4,384,538	\$	6,475,346	\$	6,475,346	\$	6,475,346			
Highland Park & Whitford HVAC	\$	1,402,000	\$	11,008,407	\$	9,148,865	\$	11,008,407	\$ 676,528	6.5%	Current budget increased by \$1.9M based on GMP for the work at Whitford
HVAC Controls User Interface Upgrade	\$	180,000	\$	180,000	\$	180,000	\$	180,000			
New Schools Post-Warranty Fund	\$	-	\$	150,000	\$	150,000	\$	150,000			
Barnes Roof & HVAC	\$	592,000	\$	1,088,000	\$	1,088,000	\$	1,088,000	\$ 108,800	11.1%	
Raleigh Park HVAC & Electrical	\$	437,000	\$	2,420,000	\$	3,247,000	\$	3,247,000	\$ 245,000	11.3%	Status marked as "Watchlist" as EAC projection exceed current budget
Raleigh Park Sewer	\$	47,000	\$	250,000	\$	250,000	\$	250,000			Scheduled to begin 2021
Terra Linda Repipe and Restroom Remodel	\$	1,068,000	\$	1,736,000	\$	1,736,000	\$	1,736,000	\$ 173,600	11.1%	
AHS Fire Alarm Replacement	\$	-	\$	150,000	\$	-	\$	150,000			
Maint Dept Repair & Improvement Projects*	\$	6,881,422	\$	6,976,762	\$	6,881,422	\$	6,976,762			
Repair Projects Total	\$	41,125,865	\$	88,425,925	\$	87,471,332	\$	89,252,925			
Repair Program Balance Available	\$	56,874,135	\$	6,002,465	\$	6,587,594	\$	5,175,465			
Repair Program EAC Balance	\$	-	\$		\$	25,800,000	<u> </u>	25,800,000			
Repair Program Budget (Less Transfers In/Out)	\$	98,000,000		94,428,390		119,858,926	\$	120,228,390			
Budget and Est @ Comp. will increase each month as addition	nal Mainte	enance Dept.	manage	ed Repair Projec	ts are	scheduled.					
Fransfer Tracking			1								
nitial Budget	\$	98,000,000									
SHS Repairs	\$	(1,881,416)									
SHS Emergency Elect	\$	745,833									
Capital Center Building Repairs	\$	(2,280,000)									
Capital Center Building Repairs	\$	1,090,725									
Fransfer From District Wide Communications System	\$	81,970									
SB 1149 Reimbursements	\$	2,623,511									
ETO Reimbursements	\$	49,661									
Additional Funding - Bethany Repipe - Approved 2.6.18	\$	1,200,000									
AHS Roofing transferred to AHS Seismic	\$	(4,053,000)									
Door Replacement(s) transferred to Security Upgrades	\$	(9,446)									
Additional Funding - AHP Roof - Approved 12.13.18	\$	650,000									
Fransfer from Seismic Upgrades - Cedar Mill	\$	166,052	l								
Fransfer from contingencies for Post-Warranty Fund	\$	150,000	l								
Cooper Mnt Roofing transferred to Cooper Mnt Seismic	\$	(128,000)	l -								
Beaver Acres Roofing transferred to Gooper Mnt Seismic			l								
	\$	(1,138,000)	l								
					1						
Additional Funding - Hiteon Flood Rebuild - Approved 7.24.19	\$	105,000									
Additional Funding - Hiteon Flood Rebuild - Approved 7.24.19 Beaver Acres Windows transferred to Beaver Acres Seismic	\$	(605,000)									
Additional Funding - Hiteon Flood Rebuild - Approved 7.24.19 Beaver Acres Windows transferred to Beaver Acres Seismic Beaver Acres Re-Pipe transferred to Beaver Acres Seismic	\$	(605,000) (489,500)									
Additional Funding - Hiteon Flood Rebuild - Approved 7.24.19 Beaver Acres Windows transferred to Beaver Acres Seismic	\$ \$ \$	(605,000)									

2014 Bond Program Financial Status Report District-Wide Repair Projects Budget Allocation Rate

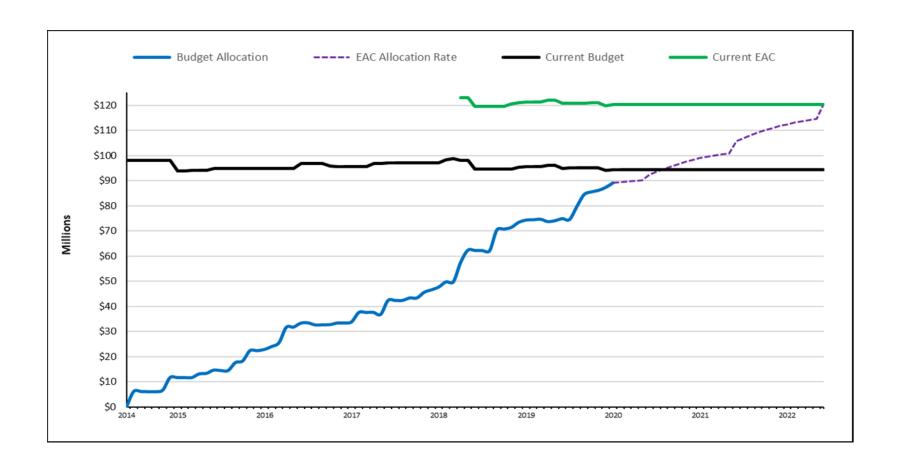

2014 Bond Program Financial Status Report Seismic Projects

Seismic Projects	Ori	ginal Budget	evised Approved Current Budget	F	Dec-19 st @ Comp	F	Jan-20 Est @ Comp		tingency ince	Budget Summary Notes
			 Janent Baaget		.st @ comp	_	est @ Gomp	Duit		
A/E Scoping/Surveys	\$	-	\$ 222,058	\$	222,058	\$	222,058	\$ -		In Close-Out; Study completed 2019
Aloha HS	\$	1,732,898	\$ 19,339,227	\$	19,339,227	\$	19,339,227	\$1,767,271	10.1%	Current contingency increased by +\$383K due to favorable bids for hallwa flooring work
Beaver Acres ES	\$	1,714,444	\$ 8,232,283	\$	8,232,283	\$	8,232,283	\$ 816,300	11.0%	
Beaverton HS	\$	246,184	udget Transferred Seismic Program)			,				Scope completed via BHS Gym Ceiling project
Cedar Mill ES	\$	144,771	Budget Moved to Facility Repairs)							Scope completed via Cedar Mill Roof & HVAC project
Cooper Mt. ES	\$	361,703	\$ 3,320,475	\$	3,320,475	\$	3,320,475			Scheduled to begin 2021
(Projects Financially Complete)										
Seismic Projects Total	\$	4,200,000		-			31,114,043			
TAPS Seismic Grant	\$	-	\$ (22,545)	\$	(22,545)		(22,545)			
AHS Seismic Rehabilitation Grant	\$	-	\$ (2,500,000)	\$	(2,500,000)	\$	(2,500,000)			
Beaver Acres Seismic Rehabilitation Grant	\$	-	\$ (2,500,000)	\$	(2,500,000)	\$	(2,500,000)			
Cooper Mnt Seismic Rehabilitation Grant	\$	-	\$ (2,337,360)	\$	(2,337,360)	\$	(2,337,360)			
Seismic Program Bond Cost Balance	\$	4,200,000	\$ 23,754,138	\$	23,754,138	\$	23,754,138			
Seismic Program Less Transfers In/Out	\$	23,754,138								
Transfer Tracking										
Initial Budget	\$	4,200,000								
Program Escalation	\$	1,006,740								
AHS Roofing - From Facility Repairs	\$	575,193								
Beaver Acres Roofing - From Facility Repairs	\$	1,138,000								
AHS Roofing - Balance From Facility Repairs	\$	3,477,807								
Program Reserve - Approved by School Board 6.18.18	\$	5,450,000								
Transfer to Facility Repairs - Cedar Mill Cooper Mnt Roofing - From Facility Repairs	\$	(166,052) 128,000								
Program Reserve - Approved by School Board 10.28.19		6,849,950								
Beaver Acres Windows - From Facility Repairs	\$	605,000								
Beaver Acres Re-pipe - From Facility Repairs	\$	489,500								
Balance		23,754,138								

2014 Bond Program Learning Technology/Classroom Systems and Critical Equipment Purchases January 31, 2020

		Le	earning Technolo	ogy/Classroom S	Systems (\$56 Mi	illion)
Project Name	Total Budget Project To Date me Project % Complete Expenditures				2019-20 Expenditures as of 1/31/2020	Annual Description of Expenditures
Networking Upgrades	\$ 9,132,995	59%	\$ 5,351,262	\$ 430,038	\$ 148,305	Maintaining current wireless networking capacity and addressing specific use cases. For 2019-20, we are expanding wireless access to outdoor spaces at the high schools including athletic fields, press boxes and concession stands. We will be preparing the school layer 2 switch replacement project.
Digital Curriculum Development	\$ 5,382,763	66%	\$ 3,558,408	\$ 716,000	\$ 323,644	Salary for five curriculum developers (5.0 FTE)
Future Ready Schools	\$ 31,485,163	77%	\$ 24,134,796	\$ 5,598,052	\$ 3,247,684	1:1 Chromebook replacement high school students. We are preparing for Chromebook replacement for middle school students and elementary students in grades 3-5.
Technology Modernization	\$ 2,961,479	57%	\$ 1,690,779	\$ 894,744	\$ 124,044	Electrical, physical, and network upgrades at Central Office Data Center. Business Continuity plans continue to be updated yearly. 2019 Security Audit is complete and IT staff are building project plans to address discovered security risks.
Other Technology/Curricum Projects	\$ 7,037,600	96%	\$ 6,764,505	\$ -	\$ -	Completed Technology/Curriculum Projects. Includes: student laptop replacements in 2014-15, high school science technology in 2015-16, positive change grants 2014-15 through 2016-17.
Learning Technology/ Classroom Systems Total	1.5 56.000.000	74%	\$ 41,499,750	\$ 7,638,834	\$ 3,843,677	

2014 Bond Program Learning Technology/Classroom Systems and Critical Equipment Purchases January 31, 2020

				Critica	l Eq	uipment (\$2	4 M	illion)	
Project Name	Total Budget Project		% Complete	Project To Date Expenditures		2019-20 Budget	2019-20 Expenditures as of 1/31/2020		Annual Description of Expenditures
Buses	\$	16,000,000	88%	\$ 14,103,131	\$	3,763,680	\$	1,866,811	Approximately \$2 million/year over eight years. In first year, \$4.25 million will be spent and \$2million/year will be spent in years two through five. In year six, approximately \$3.75 million will be spent. \$0 will be spent in the eighth year.
Copiers	\$	2,343,215	64%	\$ 1,506,993	\$	350,000	\$	113,777	Approximately \$375,000/year over eight years.
Athletic Equipment	\$	1,021,737	16%	\$ 167,764	\$	203,973	\$	-	Approximately \$100,000/year over three years beginning in year 2. \$75,970 was transferred in year 2 to the Scoreboard Replacements Project. An additional \$800,000 will be split over years six through eight.
Maintenance Equipment	\$	2,289,219	26%	\$ 589,968	\$	555,000	\$	44,968	Approximately \$120,000/year over four years beginning in year 2. Year 2 will have \$185,000. An additional \$1.7 million will be split over the final three years of the bond, beginning in year six.
Early Learning Playground Equipment	\$	27,366	34%	\$ 9,366	\$	6,000	\$	-	Playground equipment for Early Learning program at seven elementary schools.
Other Equipment Purchases	\$	2,318,463	100%	\$ 2,318,462	\$	-	\$		Other critical equipment purchases as needed. Purchase of \$15,000 towards new locker banks at Stoller in 14-15, \$250,000 towards new musical instruments in 14-15 and 15-16, \$184,050 for cafeteria table replacements in 15-16, \$1,397,733 for classroom furniture for full day kindergarten in 2015-16, \$344,973 for high school scoreboard replacements in 2015-16 and 2016-17, \$121,066 towards BSD's portion of shock pad installation at SW Quadrant Park with THPRD in 2016-17 and InTouch Printers in 2018.
Critical Equipment Total	\$	24,000,000	78%	\$ 18,695,684	\$	4,878,653	\$	2,025,556	
Grand Total	\$	80,000,000	75%	\$ 60,195,434	\$	12,517,487	\$	5,869,233	
Total Bond Funds Remaining	\$	19,804,566							

