


Bond Program Status Report

Through November 2019

2014 Bond Program Executive Summary

November 2019

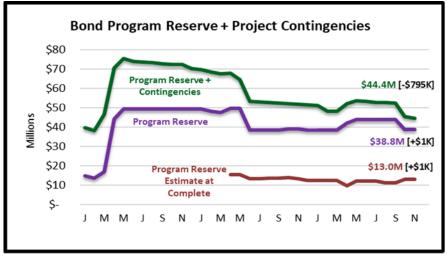

Bond Program Reserve = Funding available to the Bond Program but not yet allocated to a project Project Contingencies = Funding contained within an approved project budget

Bond Program Funding Total		\$ 806,803,383
Revised Approved Current Budget	-	\$ 768,024,648
Bond Program Reserve		\$ 38,778,735
Bond Program Reserve		\$ 38,778,735
Net Contingency Balance	+	\$ 5,622,680
Bond Program Reserve + Contingencies		\$ 44,401,415
Bond Program Funding Total		\$ 806,803,383
Program Estimate at Complete (EAC)	-	\$ 793,824,648
■ Projected Program Reserve Estimate at Complete		\$ 12,978,735

Overall Program Perspective

MWSDVE Change:

Consultants: -0.1%; Contractors: no change; Apprenticeship: no change

MWSDVE Participation:

Consultants: 14.8%; Contractors: 13.3%; Apprenticeship: 20%

Budget Perspective

This month the overall Program Reserve increased by +\$1K, while the Reserve + Project Contingencies decreased by (\$795K). All projects remain within their current approved budgets. Primary cost events were:

- ACMA's current contingency decreased by \$615K due to unforeseen site conditions involving the removal of soft soils and an abandoned underground oil tank.
- Miscellaneous contingency changes occurred on several projects and resulted in a total forecasted contingency decrease of \$180K.
- West TV Roof's current budget increased by \$557K, as approved by the Chief Facilities Officer in accordance with the Cost Management and Control Plan. The budget increase was necessary to cover final water and mold remediation costs. Staff have submitted an insurance claim with the general contractor to recoup costs.
- Raleigh Park HVAC and Electrical's estimate at complete increased by \$827K based on current project cost estimates.

Schedule Perspective

- Design is in full swing on several projects for Summer 2020, and staff are preparing for a busy bidding season. The team is hoping to hit the market early and have most major construction contracts in place by March.
- Site work continues at ACMA. First slab pours have been completed, and underground utility work is in progress.
- Five Oaks' Phase 5 (west classroom wing) work is ongoing, and Phase 6 (special education wing) early demo has begun.
- Phase 2 surveys for the Interior Classroom Locks project are ongoing. The surveys should be completed by early-January, at which point the team will analyze the results and begin planning/scheduling the work.
- A contract is in place for cameras at the high schools as part of the Security Upgrades project. Work is set to begin over Winter Break.











/E	COLLABORATI		
----	-------------	--	--


Project Name	Scope Summary	Procurement Type	Current Budget	Construction Start	Construction Finish
ACMA	(Continued) Demolition and replacement of existing building	Design - Bid - Build	\$37,570,155.00	7/2019	6/2021
Aloha High School (HS) Seismic	(Continued) Seismic structural upgrades; building re-roof	CM/GC	\$19,339,227.00	6/2019	8/2020
Auditorium Upgrades	(Continued) Auditorium upgrades across District HS; includes: stage rigging (1), step/aisle lighting (multiple), misc. safety upgrades (1), production lighting (1)	Design - Bid - Build	\$6,475,346.00	8/2017	8/2020
Barnes Elementary School (ES) HVAC/Roof	HVAC upgrade; building re-roof	Design - Bid - Build	\$1,088,000.00	6/2020	8/2020
Beaver Acres ES Seismic	Seismic structural upgrades; building re- roof; building re-pipe; window replacements	CM/GC	\$7,137,783.00	6/2020	8/2020
Conestoga Middle School (MS) Clocks	Replacement of building clocks	Design - Bid - Build	\$75,000.00	6/2020	8/2020
Errol Hassell ES Restroom Remodel	Remodel of modular student restrooms	Design - Bid - Build	\$856,000.00	6/2020	8/2020
Five Oaks	(Continued) Building renovation	CM/GC	\$28,001,419.00	6/2018	8/2020
Highland Park MS HVAC	HVAC upgrade	CM/GC	\$2,874,000.00	6/2020	9/2020
Hiteon ES HVAC	HVAC controls upgrade	Design - Bid - Build	\$500,000.00	6/2020	8/2020
Hiteon ES Paging	Paging improvements	Design - Bid - Build	\$12,000.00	6/2020	8/2020
McKay ES Clocks	Replacement of building clocks	Design - Bid - Build	\$38,000.00	6/2020	8/2020
Mountain View MS Clocks	Replacement of building clocks	Design - Bid - Build	\$75,000.00	6/2020	8/2020
Nancy Ryles ES Playground	Playground structure improvements	Design - Bid - Build	\$70,000.00	6/2020	8/2020
Oak Hills ES Restroom Remodel	Remodel of student (2 sets) and staff (2 sets) restrooms	Design - Bid - Build	\$849,000.00	6/2020	8/2020
Raleigh Hills ES Freezer Replacement	Kitchen walk-in freezer replacement	Design - Bid - Build	\$300,000.00	6/2020	8/2020
Raleigh Park ES HVAC/Electrical	HVAC and Electrical upgrades	Design - Bid - Build	\$2,420,000.00	6/2020	9/2020
Raleigh Park ES Sewer	Replacement of existing sewer line	Design - Bid - Build	\$250,000.00	6/2020	9/2020
Rock Creek ES Flooring	Replacement of existing gym and hallway flooring	Design - Bid - Build	\$136,000.00	6/2020	8/2020
Security Upgrades Interior Locks	(Continued) Replacement of current door hardware with push button locks; additional areas of refuge currently being scoped	Design - Bid - Build	\$2,000,000.00	8/2018	TBD
Security Upgrades	(Continued) Installation of cameras and fencing at HS; Phase 4 perimeter hardening	Multiple	\$14,601,033.00	9/2015	8/2020
Terra Linda ES Re-	Domestic water re-pipe; remodel of	Design - Bid - Build	\$1,736,000.00	6/2020	9/2020
pipe/Restroom Remodel Whitford MS HVAC/Roof	student bathrooms HVAC upgrade; building re-roof	CM/GC	\$5,052,500.00	6/2020	9/2020

District Goal: WE Empower all students to achieve post-high school success.

"The District prohibits discrimination and harassment based on any basis protected by law, including but not limited to, an individual's actual or perceived race, color, religion, sex, sexual orientation, gender identity, gender expression, national or ethnic origin, marital status, age, mental or physical disability, pregnancy, familial status, economic status, veteran status, or because of a perceived or actual association with any other persons within these protected classes."

School Bond Program 2020 Activity Map



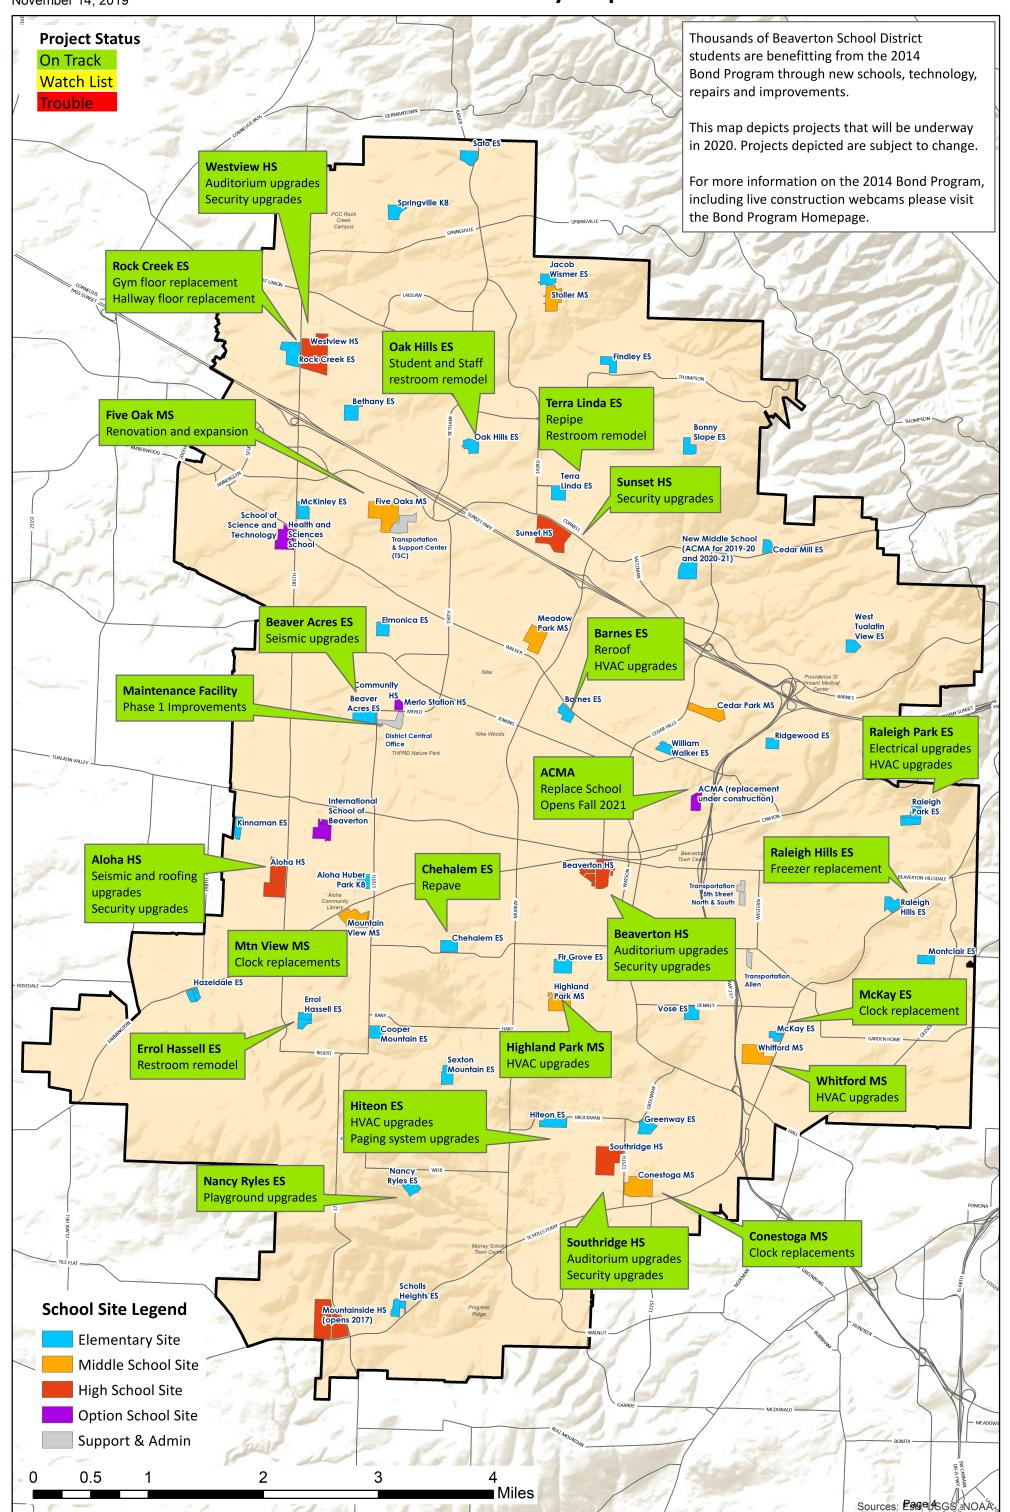

2014 Bond Program Scorecard November 2019

Performance Key

Green = On Track

Yellow = Watchlist

Red = Trouble

Gray = Milestone Complete

(Date) = Target


Date = Actual

N/A = Not Applicable


Current Performance Metrics	William Walker Replacement	ACMA Replacement	Five Oaks Renovation	Maintenance Facility	Aloha High School Seismic & Roofing	Highland Park & Whitford HVAC	West TV Roof	Cedar Mill Roof & HVAC	Beaver Acres Seismic & Renovation	Raleigh Park HVAC & Electrical	Barnes Roof & HVAC	Terra Linda Repipe
Overall Budget Performance	On Track	On Track	Watchlist	On Track	On Track	Watchlist	On Track	On Track	On Track	Watchlist	On Track	On Track
Budget Percent Complete	91.00%	22.00%	65.00%	76.00%	27.00%	4.00%	54.00%	72.00%	0.00%	2.00%	1.00%	4.00%
Overall Schedule Performance	On Track	On Track	On Track	On Track	On Track	On Track	On Track	On Track	On Track	On Track	On Track	On Track
Schedule Percent Complete	99.00%	26.00%	59.00%	60.00%	35.00%	0.00%	95.00%	99.00%	0.00%	0.00%	0.00%	0.00%
Schedule Milestones	William Walker Replacement	ACMA Renovation	Five Oaks Renovation	Maintenance Facility	Aloha High School Seismic & Roofing	Highland Park & Whitford HVAC	West TV Roof	Cedar Mill Roof & HVAC	Beaver Acres Seismic & Renovation	Raleigh Park HVAC & Electrical	Barnes Roof & HVAC	Terra Linda Repipe
Design Team Contracted	11-2016	5-2016	6-2016	6-2016	9-2018	9-2018	11-2018	9-2018	8-2019	8-2019	8-2019	7-2019
Design - Schematic Design	6-2017	3-2018	10-2017	3-2017	11-2018	10-2018	12-2018	10-2018	10-2019	(12-2019)	10-2019	9-2019
Design - Design Development	8-2017	8-2018	11-2017	10-2018	1-2019	11-2018	1-2019	11-2018	11-2019	(1-2020)	11-2019	(1-2019
Design - Construction Documents	10-2017	2-2019	5-2018	1-2019	3-2019	3-2019	2-2019	1-2019	(1-2020)	(2-2020)	(12-2019)	(1-2020)
Permitting - Land Use	9-2017	1-2019	3-2018	1-2019	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Permitting - Site Development	7-2018	5-2019	7-2018	4-2019	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Permitting - Building	8-2018	7-2019	6-2018	4-2019	11-2019	(5-2020)	8-2019	5-2019	(5-2020)	(6-2020)	(5-2020)	(6-2020)
Construction - Contract Award	1-2018	5-2019	9-2017	7-2017	2-2019	8-2019	7-2019	3-2019	(2-2020)	(2-2020)	(2-2020)	(3-2020)
Construction - Start	5-2018	7-2019	6-2018	3-2019	6-2019	(6-2020)	8-2019	6-2019	(6-2020)	(6-2020)	(6-2020)	(6-2020)
Construction - Finish	8-2019	(8-2021)	(8-2020)	(8-2020)	(8-2020)	(9-2020)	10-2019	8-2019	(8-2020)	(8-2020)	(8-2020)	(9-2020)
Owner Activities - FF&E Ordered	3-2019	(2-2021)	3-2019	N/A	N/A	N/A	N/A	N/A	(6-2020)	N/A	N/A	N/A
Owner Activities - FF&E Delivered	8-2019	(5-2021)	(8-2020)	N/A	N/A	N/A	N/A	N/A	(8-2020)	N/A	N/A	N/A
Owner Activities - Occupancy	8-2019	(6-2021)	(8-2020)	(8-2020)	(8-2020)	(9-2020)	10-2019	8-2019	(8-2020)	(9-2020)	(9-2020)	(9-2020)
Project Complete (Month - Year)	8-2019	(8-2021)	(8-2020)	(8-2020)	(8-2020)	(8-2020)	10-2019	8-2019	(8-2020)	(9-2020)	(9-2020)	(9-2020)
Equity Goals												
Participation	Target %	Current %	Change %	i								
MWSDVE - Consultants	10.0%	14.8%	-0.10%	1								
MWSDVE - Contractors	10.0%	13.3%	No change	1								
Apprenticeship	10.0%	20.0%	No change	1								

2014 Construction Bond Program

Equity Performance November 2019 Report

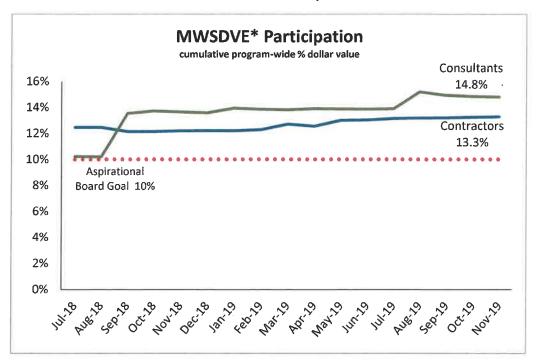

*Minority, Women and Service Disabled Veteran Owned Enterprises

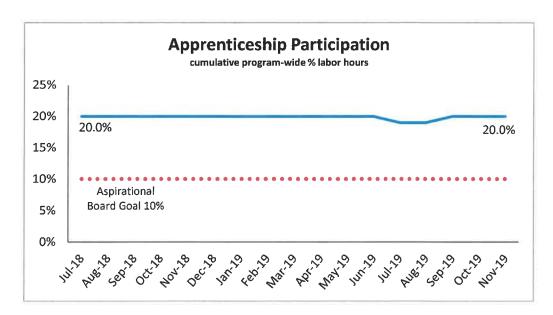

2014 Bond Program Financial Status Report Financial Summary

Project List	 ginal Budget Illocations	sed Approved rrent Budget	Oct-19 Est @ Cor		E	Nov-19 Est @ Comp	Net Contingen	псу Ва	alance	Budget Summary Notes
ACMA Replacement	\$ 28,300,000	\$ 37,570,155	\$ 37,57	0,155	\$	37,570,155	\$ 3,161,284		9.2%	Current contingency decreased by (\$615K) due to unforeseen soft soils and underground oil tank removal
AHS Title IX Compliance	\$ 2,000,000	\$ 3,453,433	\$ 3,45	3,433	\$	3,453,433				Completed; Final Cost
Capital Center Improvements & Data Center	\$ 5,000,000	\$ 12,820,187	\$ 12,82	0,187	\$	12,820,187				Completed; Final Cost
District-Wide ADA Compliance	\$ 2,000,000	\$ 2,000,000	\$ 2,00	0,000	\$	2,000,000				Projects in Process
District-Wide Communication System	\$ 7,200,000	\$ 5,282,072	\$ 5,28	2,072	\$	5,282,072				Completed; Final Cost
District-Wide Facility Repairs	\$ 98,000,000	\$ 95,153,426	\$ 120,90	6,424	\$	120,953,426				Current budget increased by +\$47K due to additional SB1149 reimbursement
District-Wide HVAC Controls	\$ 800,000	\$ 800,000	\$ 80	0,000	\$	800,000				Projects in Process
Domestic / Fire Line Separation	\$ 800,000	\$ 977,120	\$ 97	7,120	\$	977,120				
Five Oaks MS Renovation & Expansion	\$ 21,100,000	\$ 28,001,419	\$ 28,00	1,419	\$	28,001,419	\$ 75,202		0.3%	
Green Energy Technology	\$ 5,000,000	dget Moved to her Projects)								Scope completed via new schools and rebuilds
Hazeldale K-5 Replacement	\$ 24,600,000	\$ 31,756,091	\$ 31,75	6,091	\$	31,756,091	\$ 120,024			In Close-Out; Construction Completed 2018
IT Data Center @ Capital Center	\$ 2,900,000	dget Moved to CC Project)								Scope completed via Capital Center Improvements
Kitchen Improvements	\$ 800,000	\$ 977,120	\$ 97	7,120	\$	977,120				Projects in Process
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000	\$ 7,800,000	\$ 7,80	0,000	\$	7,800,000				In Close-Out; Purchase completed 2019
Maintenance Facility Improvements Phase I	\$ 10,000,000	\$ 11,263,990	\$ 11,26	3,990	\$	11,263,990	\$ 179,948		1.6%	
McKay ADA Improvements	\$ 400,000	\$ 634,540	\$ 63	4,540	\$	634,540				Completed; Final Cost
New HS: Mountainside	\$ 109,000,000	\$ 184,135,294	\$ 184,13	5,294	\$	184,135,294	\$ 322,070			In Close-Out; Construction Completed 2017
New ES: Sato K5	\$ 25,000,000	\$ 38,175,000	\$ 38,17	5,000	\$	38,175,000	\$ 83,666			In Close-Out; Construction Completed 2017
New MS @ Timberland	\$ 51,600,000	\$ 61,371,096	\$ 61,37	1,096	\$	61,371,096	\$ 261,073			Construction completed 2016; remaining budget reserved for final outfitting
Raleigh Hills K-8 Improvements	\$ 9,700,000	\$ 1,419,490	\$ 1,41	9,490	\$	1,419,490				Completed; Final Cost
Raleigh Hills K-8 Improvements (Funding Hold)	\$ -	\$ 11,821,753	\$ 11,82	1,753	\$	11,821,753				
Security Upgrades	\$ 10,000,000	\$ 14,621,670	\$ 14,62	1,670	\$	14,621,670				
Seismic Upgrades	\$ 4,200,000	\$ 22,659,638	\$ 22,65	9,638	\$	22,659,638				

2014 Bond Program Financial Status Report Financial Summary

SHS Tille IX Compilance SHS TILLE IX SHS TILLE SHS TILLE SHS TILLE IX SHS TILLE SHS TILLE SHS TILLE IX SHS TILLE SHS TILLE IX SHS TILLE SHS TILLE SHS TILLE IX SHS TILLE SHS TILLE SHS TILLE IX SHS TILLE	Project List		al Budget cations		rised Approved urrent Budget	E	Oct-19 Est @ Comp		Nov-19 Est @ Comp	Net Continger	ncy Balance	Budget Summary Notes
Springsylle K-8 Improvements												
Value K-6 Replacement	SHS Title IX Compliance	\$	2,000,000	\$	4,285,317	\$	4,285,317	\$	4,285,317			Completed; Final Cost
William Walker K-5 Replacement \$ 24,600,000 \$ 36,684.200 \$ 36,684.200 \$ 1,419,413 4.5%	Springville K-8 Improvements	\$	2,000,000	\$	510,016	\$	510,016	\$	510,016			Completed; Final Cost
Added Projects \$	Vose K-5 Replacement	\$ 2	24,800,000	\$	33,846,280	\$	33,846,280	\$	33,846,280			Completed; Final Cost
Program Contingency	William Walker K-5 Replacement	\$ 2	24,600,000	\$	36,684,200	\$	36,684,200	\$	36,684,200	\$ 1,419,413	4.0%	
Program Inflation	Added Projects	\$	-	\$	4,016,007	\$	4,016,007	\$	4,016,007			
Pre-Band Expenditure Reimbursements	Program Contingency	\$ 4	45,400,000									
Bond Management Costs \$ 20,000,000 \$ 30,990,506 \$ 30,990,506 \$ 30,990,506 \$ 30,990,506 \$ \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 4,000,000 \$ 56,000,000 \$ 56,000,000 \$ 56,000,000 \$ 56,000,000 \$ 56,000,000 \$ 56,000,000 \$ 56,000,000 \$ 24,000,0	Program Inflation	\$ 5	52,800,000									
Section Substance Costs Section Sectio	Pre-Bond Expenditure Reimbursements	\$	1,000,000	\$	998,828	\$	998,828	\$	998,828			Completed; Final Cost
Construction Subtotal \$ 600,000,000 \$ 688,024,648 \$ 713,777,646 \$ 713,824,648 \$ 5,622,680	Bond Management Costs	\$ 2	20,000,000	\$	30,990,506	\$	30,990,506	\$	30,990,506			
Learning Technology	Bond Issuance Costs	\$	6,000,000	\$	4,000,000	\$	4,000,000	\$	4,000,000			
Critical Equipment \$ 24,000,000	Construction Subtotal	\$ 600	0,000,000	\$	688,024,648	\$	713,777,646	\$	713,824,648	\$ 5,622,680		
Tech & Equip Subtotal \$80,000,000 \$80,000,000 \$80,000,000 \$00,	Learning Technology	\$ 5	56,000,000	\$	56,000,000	\$	56,000,000	\$	56,000,000			
Grand Totals \$ 680,000,000 \$ 768,024,648 \$ 793,777,646 \$ 793,824,648 \$ 5,622,680 Contingency Balance change of (\$797K)	Critical Equipment	\$ 2	24,000,000	\$	24,000,000	\$	24,000,000	\$	24,000,000			
Added Funding to Bond Program Bond Premium (First Bond Sale) \$ 63,295,961	Tech & Equip Subtotal	\$ 80	0,000,000	\$	80,000,000	\$	80,000,000	\$	80,000,000			
Bond Premium (First Bond Sale) \$ 63,295,961	Grand Totals	\$ 680	0,000,000	\$	768,024,648	\$	793,777,646	\$	793,824,648	\$ 5,622,680		Contingency Balance change of (\$797K)
Bond Premium (Second Bond Sale) \$ 30,270,107	Added Funding to Bond Program											
Interest Earnings (First Bond Sale) \$ 5,340,214 Interest Earnings (Second Bond Sale) \$ 13,236,261 Other Additional Funding (see Tab) \$ 14,660,840 Other Additional Funding (see Tab) \$ 126,803,383 Total Funding Increased by \$48K GRAND TOTAL 2014 BOND FUNDING \$ 806,803,383 Total Funding Increased by \$448K Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of \$1K	Bond Premium (First Bond Sale)	\$ 6	63,295,961									
Interest Earnings (Second Bond Sale)	Bond Premium (Second Bond Sale)	\$ 3	30,270,107									
Other Additional Funding (see Tab) \$ 14,660,840 Grand Total Added Funding \$ 126,803,383 GRAND TOTAL 2014 BOND FUNDING \$ 806,803,383 Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of +\$1K	Interest Earnings (First Bond Sale)	\$	5,340,214									
Grand Total Added Funding \$ 126,803,383 Total Funding increased by +\$48K GRAND TOTAL 2014 BOND FUNDING \$ 806,803,383 Total Funding increased by +\$48K Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of +\$1K	<u> </u>	\$	13,236,261									
GRAND TOTAL 2014 BOND FUNDING \$ 806,803,383 Total Funding increased by +\$48K Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of +\$1K	Other Additional Funding (see Tab)	\$	14,660,840									
Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of +\$1K	Grand Total Added Funding	\$ 126	,803,383									
Program Reserve \$ 38,778,735 \$ 12,977,365 \$ 12,978,735 Program Reserve change of +\$1K	GRAND TOTAL 2014 BOND FUNDING	\$ 806	803 383									Total Funding increased by +\$48K
		Ψ 000	,,000,000	\$	38 778 735	\$	12 977 365	\$	12 978 735			·
	Program Reserve + Project Contingencies			Ψ	55,115,155	<u> </u>	,577,500	Ψ	. 1,0 ,0 ,, 100		\$ 11 101 115	

2014 Bond Program Financial Status Report Additional Funding Allocations to Bond Program

Source	Funding	Assigned to Projects	Assigned to gram Reserve	Budget Summary Notes
Remaining 2006 Bond Savings	\$ 576,615	Mountainside HS	\$ -	
Capital Center Rent Revenue Balance	\$ 433,385	Mountainside HS	\$ -	
Construction Excise Tax Revenue	\$ 1,130,655	Capital Center	\$ -	
Construction Excise Tax Revenue forecasted to 2021	\$ 5,021,577		\$5,021,577	
THPRD reimb.	\$ 449,783		\$ 449,783	
SB 1149 reimb.	\$ 2,404,047	District-wide Repairs	\$ -	
ETO reimb.	\$ 1,117,272	District-wide Repairs	\$ 1,067,611	
Facility grants	\$ 3,027,507		\$ 3,027,507	
Sato: TVWD Reimbursement	\$ 500,000	Sato K-5	\$ -	
TOTAL	\$14,660,840		\$9,566,478	

2014 Bond Program Financial Status Report Added Projects


Added Projects	Approved by & Date	Original Budget	Revised Appr Current Bud		Oct-19 st @ Comp	E	Nov-19 st @ Comp	Net Contingency Balance		Budget Summary Notes
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$ 99	9,368	\$ 99,368	\$	99,368	\$	-	Completed; Final Cost
Portable Relocations 2014	Sr LT 5/20/14		\$ 59	1,685	\$ 591,685	\$	591,685	\$	-	Completed; Final Cost
Portable Relocations 2015	Sr LT 3/2015		\$ 29	4,257	\$ 294,257	\$	294,257	\$	-	Completed; Final Cost
Title IX Projects - Group II	Sr LT 3/2015		\$ 1,030	0,697	\$ 1,030,697	\$	1,030,697	\$	-	Completed; Final Cost
Classroom Door Locks	SB 6/18/18		\$ 2,000	0,000	\$ 2,000,000	\$	2,000,000	\$	-	Budget 54% complete; phase 2 surveys ongoing
Added Projects Total		\$ -	\$ 4,010	6,007	\$ 4,016,007	\$	4,016,007			

2014 Bond Program Financial Status Report

District-Wide Repair Projects "The \$98M"

	Π		Rev	ised Approved		Oct-19	Nov-19	Ι			
Project	lni	itial Budget		rrent Budget		Est @ Comp	Est @ Comp		Net Contingency	Balance	Budget Summary Notes
Completed Projects	\$	20,368,895	\$	42,035,548	\$	33,780,734	\$ 42,035,549				Completed; Final Cost
Mountain View Roof	\$	1,245,000	\$	3,773,284	\$	4,185,000	\$ 3,773,284		Completed; Fina	al Cost	
Ridgewood HVAC and Electrical	\$	829,173	\$	4,481,531	\$	4,563,774	\$ 4,481,531		Completed; Fina	al Cost	
Projects in Close-out	\$	5,765,010	\$	16,696,848	\$	24,888,454	\$ 16,433,210	\$	948,094	6.0%	West TV Roof Current Budget increased by +\$557K after receiving the final water and mold remediation costs. Staff have submitted an insurance claim with the general contractor to recoup costs.
District-Wide Auditorium Upgrades	\$	4,384,538	\$	6,475,346	\$	6,475,346	\$ 6,475,346				
Highland Park & Whitford HVAC	\$	1,402,000	\$	7,926,500	\$	7,926,500	\$ 7,926,500	\$	37,965	0.5%	
HVAC Controls User Interface Upgrade	\$	180,000	\$	180,000	\$	180,000	\$ 180,000				
New Schools Post-Warranty Fund	\$	-	\$	150,000	\$	150,000	\$ 150,000				
Barnes Roof & HVAC	\$	592,000	\$	1,088,000	\$	1,088,000	\$ 1,088,000	\$	108,800	11.1%	
Raleigh Park HVAC & Electrical	\$	437,000	\$	2,420,000	\$	2,420,000	\$ 3,247,000	\$	240,000	11.0%	Current estimate at complete increased by +827K based on current project cost estimates
Raleigh Park Sewer	\$	47,000	\$	250,000	\$	250,000	\$ 250,000			0.0%	
Terra Linda Repipe and Restroom Remodel	\$	1,068,000	\$	1,736,000	\$	1,736,000	\$ 1,736,000	\$	173,600	11.1%	
Maint Dept Repair & Improvement Projects*	\$	6,754,138	\$	6,757,228	\$	6,754,138	\$ 6,757,228				
Repair Projects Total	\$	40,998,582	\$	85,715,471	\$	85,649,173	\$ 86,278,833				
Repair Program Balance Available	\$	57,001,418	\$	9,437,955	\$	9,457,251	\$ 8,874,593				
Repair Program EAC Balance	\$	-	\$	-	\$	25,800,000	\$ 25,800,000				
Repair Program Budget (Less Transfers In/Out)	\$	98,000,000	\$	95,153,426	\$	120,906,424	\$ 120,953,426				
*Budget and Est @ Comp. will increase each month as addition	al Mair	ntenance Dept.	mana	ged Repair Projec	ts ar	e scheduled.					
Transfer Tracking			l								
Initial Budget	\$	98,000,000									
SHS Repairs	\$	(1,881,416)									
SHS Emergency Elect	\$	745,833									
Capital Center Building Repairs	\$	(2,280,000)									
Capital Center Building Repairs	\$	1,090,725									
Transfer From District Wide Communications System	\$	81,970									
SB 1149 Reimbursements	\$	2,404,047									
ETO Reimbursements	\$	49,661									
Additional Funding - Bethany Repipe - Approved 2.6.18	\$	1,200,000	l -								
AHS Roofing transferred to AHS Seismic	\$	(4,053,000)									
Door Replacement(s) transferred to Security Upgrades	\$	(9,446)	 		-						
	\$	(9,446) 650.000									
Additional Funding - AHP Roof - Approved 12.13.18					-						
Transfer from Seismic Upgrades - Cedar Mill	\$	166,052	<u> </u>		-						
Transfer from contingencies for Post-Warranty Fund	\$	150,000									
Cooper Mnt Roofing transferred to Cooper Mnt Seismic	\$	(128,000)									
Beaver Acres Roofing transferred to Beaver Acres Seismic	\$	(1,138,000)									
Additional Funding - Hiteon Flood Rebuild - Approved 7.24.19		105,000									
Balance	\$	95,153,426	l								

2014 Bond Program Financial Status Report District-Wide Repair Projects Budget Allocation Rate

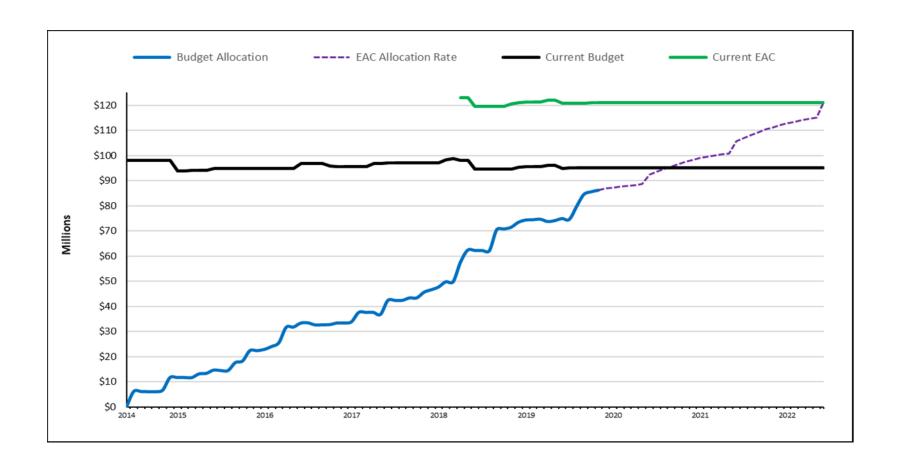

2014 Bond Program Financial Status Report Seismic Projects

Seismic Projects	Orio	ginal Budget	Rev	ised Approved		Oct-19		Nov-19	Net Con	itingency	Budget Summary Notes
Seisilic Projects	OII	gillai Buuget	C	urrent Budget	E	st @ Comp	E	est @ Comp	Bala	ance	Budget Summary Notes
A/E Scoping/Surveys	\$	-	\$	222,058	\$	222,058	\$	222,058	\$ -		In Close-Out; Study completed 2019
Aloha HS	\$	1,732,898	\$	19,339,227	\$	19,339,227	\$	19,339,227	\$1,399,271	7.8%	
Beaver Acres ES	\$	1,714,444	\$	7,137,783	\$	7,137,783	\$	7,137,783	\$ 716,800	11.2%	
Beaverton HS	\$	246,184		dget Transferred to Aloha HS)							Scope completed via BHS Gym Ceiling project
Cedar Mill ES	\$	144,771		udget Moved to acility Repairs)							Scope completed via Cedar Mill Roof & HVAC project
Cooper Mt. ES	\$	361,703	\$	3,320,475	\$	3,320,475	\$	3,320,475			Scheduled to begin 2021
(Projects Financially Complete)											
Seismic Projects Total	\$	4,200,000	\$	30,019,543	\$	30,019,543	\$	30,019,543			
TAPS Seismic Grant	\$	-	\$	(22,545)	\$	(22,545)	\$	(22,545)			
AHS Seismic Rehabilitation Grant	\$	-	\$	(2,500,000)	\$	(2,500,000)	\$	(2,500,000)			
Beaver Acres Seismic Rehabilitation Grant	\$	_	\$	(2,500,000)	\$	(2,500,000)	\$	(2,500,000)			
Cooper Mnt Seismic Rehabilitation Grant	\$	-	\$	(2,337,360)	\$	(2,337,360)	\$	(2,337,360)			
Seismic Program Bond Cost Balance	\$	4,200,000	\$			22,659,638		, , , ,			
Seismic Program Less Transfers In/Out	\$	22,659,638									
The current project budget is fixed at \$22,659,638, which											
rom the District-Wide Facility Repair project. Projections	for ad	ditional funds w	ill be f	orecasted at a late	er d	ate (dependen	t or	staff's confide	nce level) as	the project me	oves between phases.
Fransfer Tracking											
nitial Budget	\$	4.200.000									
Program Escalation	\$	1,006,740									
AHS Roofing - From Facility Repairs	\$	575,193									
Beaver Acres Roofing - From Facility Repairs	\$	1,138,000									
AHS Roofing - Balance From Facility Repairs	\$	3,477,807									
Program Reserve - Approved by School Board 6.18.18	\$	5,450,000									
Fransfer to Facility Repairs - Cedar Mill	\$	(166,052)									
Cooper Mnt Roofing - From Facility Repairs	\$	128.000									
Program Reserve - Approved by School Board 10.28.19		6,849,950									
Balance	_	22,659,638									
Balance	Ψ	,000,000								l.	

2014 Bond Program Learning Technology/Classroom Systems and Critical Equipment Purchases November 2019

			Le	arni	ing Technolo	ogy/	Classroom S	yst	ems (\$56 Mi	llion)
Project Name		tal Budget Project	% Complete		oject To Date xpenditures				2019-20 xpenditures of 11/30/2019	Annual Description of Expenditures
Networking Upgrades	\$	9,132,995	58%	\$	5,257,364	\$	430,038	\$		Maintaining current wireless networking capacity and addressing specific use cases. For 2019-20, we are expanding wireless access to outdoor spaces at the high schools including athletic fields, press boxes and concession stands. We will be preparing the school layer 2 switch replacement project.
Digital Curriculum Development	\$	5,382,763	64%	\$	3,446,826	\$	716,000	\$	212,062	Salary for five curriculum developers (5.0 FTE)
Future Ready Schools	\$	31,485,163	77%	\$	24,126,620	\$	5,598,052	\$	3,239,508	1:1 Chromebook replacement high school students. We are preparing for Chromebook replacement for middle school students and elementary students in grades 3-5.
Technology Modernization	\$	2,961,479	56%	\$	1,657,760	\$	894,744	\$	- ,	Electrical, physical, and network upgrades at Central Office Data Center. Business Continuity plans continue to be updated yearly. 2019 Security Audit is complete and IT staff are building project plans to address discovered security risks.
Other Technology/Curricum Projects	\$	7,037,600	96%	\$	6,764,505	\$	-	\$	-	Completed Technology/Curriculum Projects. Includes: student laptop replacements in 2014-15, high school science technology in 2015-16, positive change grants 2014-15 through 2016-17.
Learning Technology/ Classroom Systems Total	1.5	56,000,000	74%	\$	41,253,075	\$	7,638,834	\$	3,597,002	

2014 Bond Program Learning Technology/Classroom Systems and Critical Equipment Purchases November 2019

			Critica	l Eq	uipment (\$2	4 M	illion)	
Project Name	Total Budget Project	% Complete	oject To Date		2019-20 Budget		2019-20 spenditures f 11/30/2019	Annual Description of Expenditures
Buses	\$ 16,000,00	0 88%	\$ 14,103,131	\$	3,763,680	\$	1,866,811	Approximately \$2 million/year over eight years. In first year, \$4.25 million will be spent and \$2million/year will be spent in years two through five. In year six, approximately \$3.75 million will be spent. \$0 will be spent in the eighth year.
Copiers	\$ 2,343,21	5 64%	\$ 1,506,993	\$	350,000	\$	113,777	Approximately \$375,000/year over eight years.
Athletic Equipment	\$ 1,021,73	7 16%	\$ 167,764	\$	203,973	\$	-	Approximately \$100,000/year over three years beginning in year 2. \$75,970 was transferred in year 2 to the Scoreboard Replacements Project. An additional \$800,000 will be split over years six through eight.
Maintenance Equipment	\$ 2,289,21	9 26%	\$ 585,460	\$	555,000	\$	40,460	Approximately \$120,000/year over four years beginning in year 2. Year 2 will have \$185,000. An additional \$1.7 million will be split over the final three years of the bond, beginning in year six.
Early Learning Playground Equipment	\$ 27,36	6 34%	\$ 9,366	\$	6,000	\$	-	Playground equipment for Early Learning program at seven elementary schools.
Other Equipment Purchases	\$ 2,318,46	3 100%	\$ 2,318,462	\$	-	\$	-	Other critical equipment purchases as needed. Purchase of \$15,000 towards new locker banks at Stoller in 14-15, \$250,000 towards new musical instruments in 14-15 and 15-16, \$184,050 for cafeteria table replacements in 15-16, \$1,397,733 for classroom furniture for full day kindergarten in 2015-16, \$344,973 for high school scoreboard replacements in 2015-16 and 2016-17, \$121,066 towards BSD's portion of shock pad installation at SW Quadrant Park with THPRD in 2016-17 and InTouch Printers in 2018.
Critical Equipment Total			\$ 18,691,176	<u> </u>	4,878,653	+-	2,021,048	
Grand Total Total Bond Funds Remaining	\$ 80,000,00 \$ 20,055,74		\$ 59,944,251	\$	12,517,487	\$	5,618,050	

