


Bond Program Status Report

Through March 2022

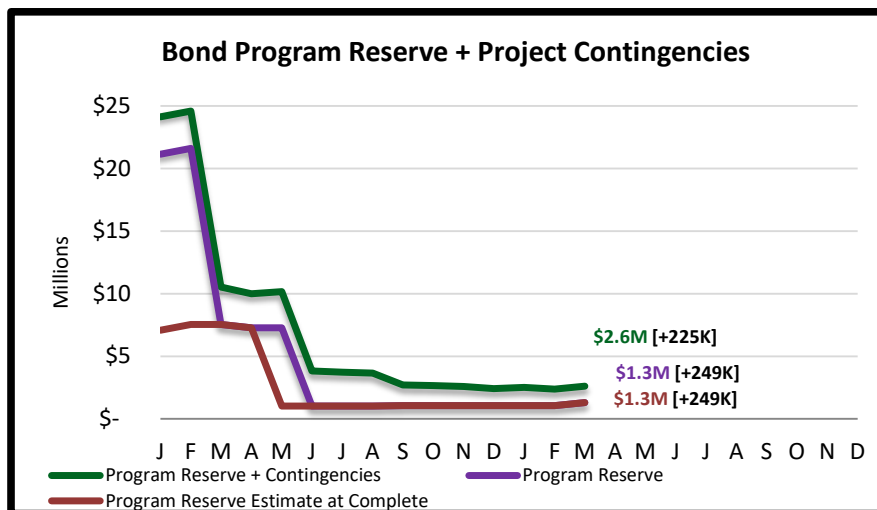

Bond Program Reserve = Funding available to the Bond Program but not yet allocated to a project
 Project Contingencies = Funding contained within an approved project budget

Bond Program Funding Total	\$	808,176,988
Revised Approved Current Budget	-	\$ 806,875,179
Bond Program Reserve	\$	1,301,809
Bond Program Reserve	\$	1,301,809
Net Contingency Balance	+	\$ 1,295,280
Bond Program Reserve + Contingencies	\$	2,597,089
Bond Program Funding Total	\$	808,176,988
Program Estimate at Complete (EAC)	-	\$ 806,875,179
Projected Program Reserve Estimate at Complete	\$	1,301,809

Budget Perspective

This month the overall Program Reserve increased by \$249K and the Reserve + Project Contingencies increased by \$225K. Repair Projects and Seismic Upgrades had minor budget changes. Primary cost events were:

- ACMA's contingency decreased by \$24k due to various closeout items including: replacing cameras in the PAC, replacing floor transitions, and adding eyewash stations.
- Transfer of funds of \$247K from Seismic Funding Hold to Repair Projects Group 1 Roofing (McKinley)
- Received SB1149 funds in the amount of \$240,585 for Five Oaks and \$8,243 for ACMA. The total of \$248,828 went to Program Reserve.
- Received ETO/SB1149 funds in the amount of \$54,794 for ISB which went to the District Wide Facility Repairs budget.

Schedule Perspective

- Construction for the Vose classroom addition started construction during Spring Break (March 20). This project is large enough that there was not enough time to complete over the summer. We have worked closely with the contractor to develop a work plan that minimizes disruption on-site.
- We are nearing completion of the conceptual design of the Raleigh Hills ES replacement. This project will be in a great place to move forward if the May 2022 bond passes.
- We are working closely with our project teams to prepare for any supply chain related delays this summer. Some availability issues seem to be improving, but costs are going up. This is going to continue to be an issue, especially with fuel costs increasing so much.


Challenges and Opportunities

- As a part of the Federal CARES act, the District has received Elementary and Secondary School Emergency Relief (ESSER), and a portion is being executed through Bond projects to help improve HVAC and air flow functions in our buildings. Current projects utilizing ESSER funds are Hiteon HVAC Controls Upgrade, 2022 HVAC Upgrade Group 1, and West TV Seismic.
- We have submitted a Seismic Rehabilitation Grant Program Application for a seismic upgrade at McKinley ES. We should know if this is successful by May of 2022. The work will take place during the summer of 2023.

2014 Bond Program

Middle School, High School & Options

September 8, 2021

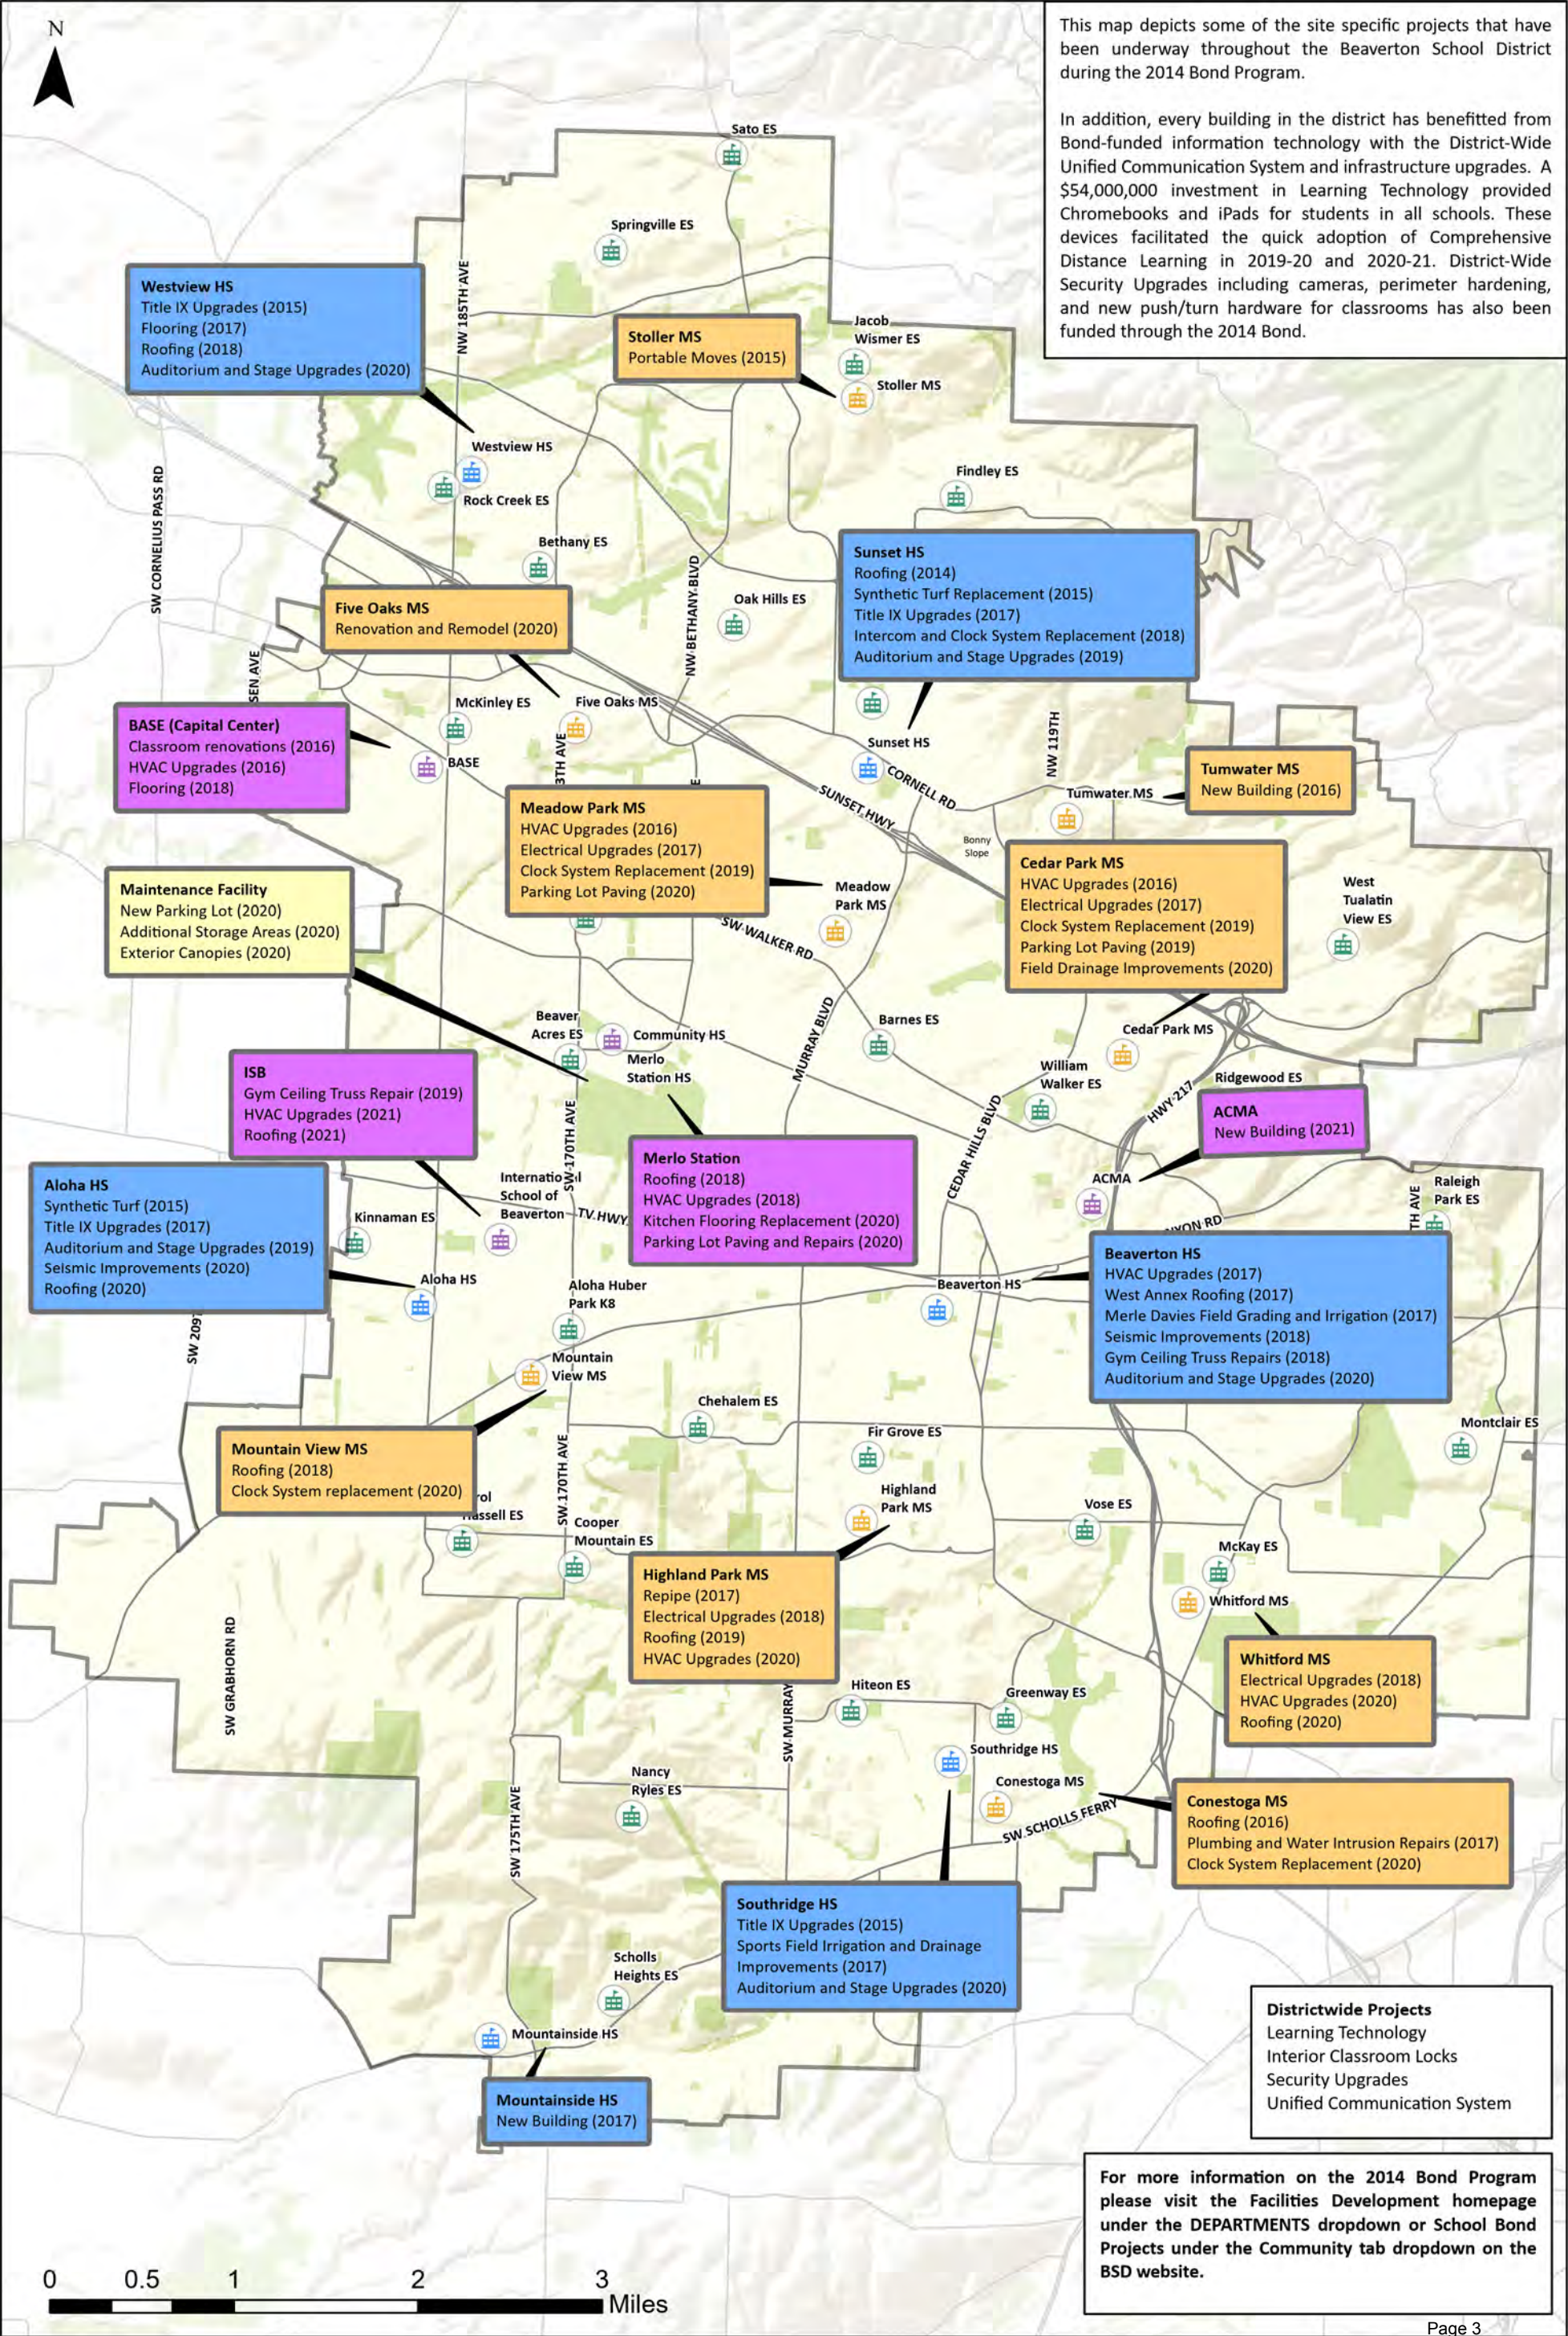

N



Scholls Heights ES
Playground Improvements (2019)

In addition, every building in the district has benefitted from Bond-funded information technology with the District-Wide Unified Communication System and infrastructure upgrades. A \$54,000,000 investment in Learning Technology provided Chromebooks and iPads for students in all schools. These devices facilitated the quick adoption of Comprehensive Distance Learning in 2019-20 and 2020-21. District-Wide Security Upgrades including cameras, perimeter hardening, and new push/turn hardware for classrooms has also been funded through the 2014 Bond.

For more information on the 2014 Bond Program please visit the Facilities Development homepage under the DEPARTMENTS dropdown or School Bond Projects under the Community tab dropdown on the BSD website.

Sources: Esri, USGS, NOAA



2014 Bond Program Scorecard

March 2022


Data as of March 31, 2022

Performance Key	
Green = On Track	
Yellow = Watchlist	
Red = Trouble	
Gray = Milestone Complete	
(Date) = Target	
Date = Actual	
N/A = Not Applicable	


Current Performance Metrics	Bethany HVAC & Roof	ISB Roof & HVAC	2021 Roofs (Montclair)	Security Upgrades: Classroom Walls	Vose Classroom Addition	2022 Repipes	2022 HVAC Upgrades Group 1
Overall Budget Performance	On Track	On Track	On Track	On Track	On Track	On Track	On Track
Budget Percent Complete	38.00%	66.00%	64.00%	25.00%	15.00%	2.00%	4.00%
Overall Schedule Performance	On Track	On Track	On Track	On Track	On Track	On Track	On Track
Schedule Percent Complete	43.00%	74.00%	60.00%	30.00%	10.00%	0.00%	0.00%
Schedule Milestones	Bethany HVAC & Roof	ISB Roof & HVAC	2021 Roof Replacements	Security Upgrades: Classroom Walls	Vose Classroom Addition	2022 Repipes	2022 HVAC Upgrades Group 1
Design Team Contracted	N/A	8-2020	6-2020	11-2020	11-2020	11-2021	3-2021
Design - Schematic Design	N/A	11-2020	7-2020	1-2021	N/A	11-2021	N/A
Design - Design Development	3-2021	12-2020	9-2020	2-2021	1-2021	1-2022	5-2021
Design - Construction Documents	4-2021	2-2021	10-2020	3-2021	2-2021	(2-2022)	6-2021
Permitting - Land Use	N/A	N/A	N/A	N/A	7-2021	N/A	N/A
Permitting - Site Development	N/A	N/A	N/A	N/A	7-2021	N/A	N/A
Permitting - Building	6-2021	4-2021	11-2020	3-2021	12-2021	(3-2022)	N/A
Construction - Contract Award	10-2020	4-2021	1-2021	6-2021	10-2021	(3-2022)	11-2021
Construction - Start	6-2021	6-2021	(6-2022)	6-2021	(3-2022)	(6-2022)	(6-2022)
Construction - Finish	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(9-2022)	(8-2022)	(8-2022)
Owner Activities - FF&E Ordered	N/A	N/A	N/A	N/A	(1-2022)	N/A	N/A
Owner Activities - FF&E Delivered	N/A	N/A	N/A	N/A	TBD	N/A	N/A
Owner Activities - Occupancy	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(8-2022)	(8-2022)	(8-2022)
Project Complete (Month - Year)	(8-2022)	(9-2022)	(8-2022)	(8-2022)	(9-2022)	(8-2022)	(8-2022)
Equity Goals							
Participation	Target %	Current %	Change %				
MWSDVE - Consultants	10.0%	18.0%	-0.20%				
MWSDVE - Contractors	10.0%	14.6%	-0.10%				
Apprenticeship	10.0%	19.0%	No change				

2014 Construction Bond Program

Equity Performance March 2022 Report

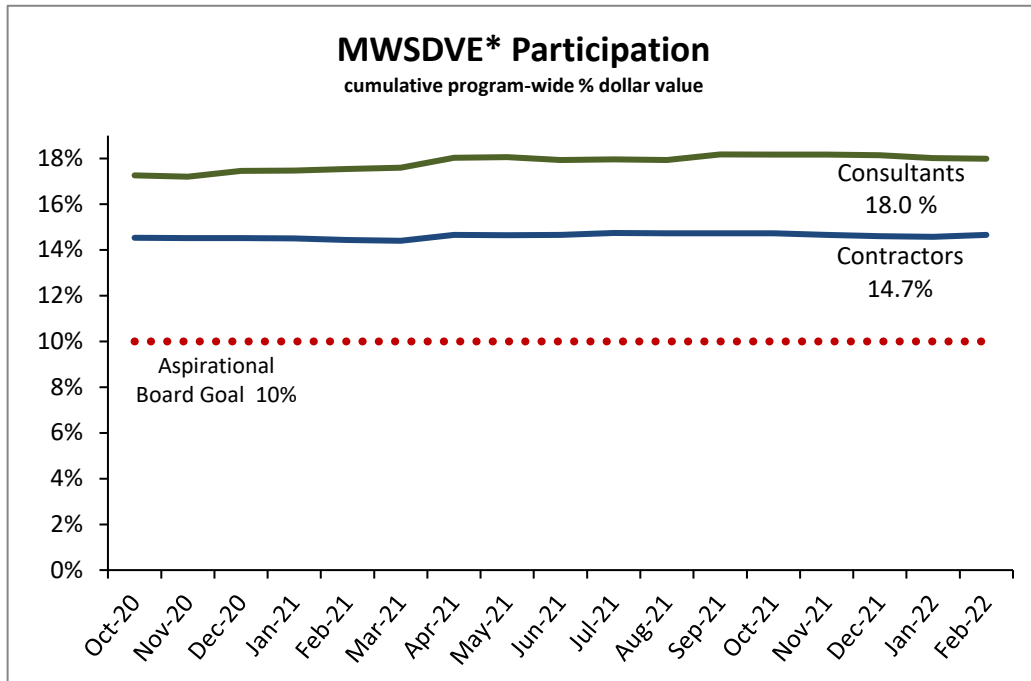

*Minority, Women and Service Disabled Veteran Owned Enterprises

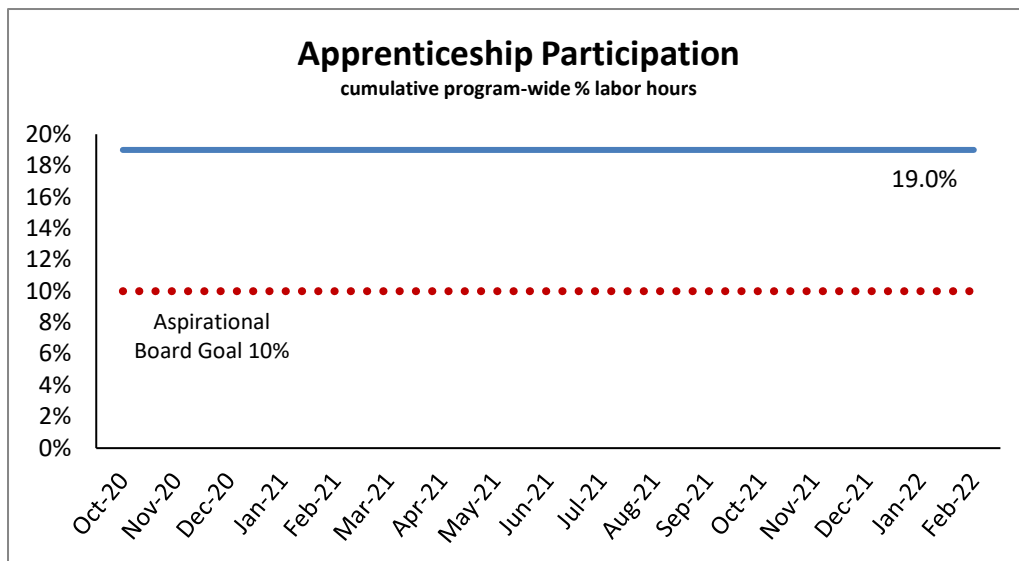

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Project List	Original Budget Allocations	Revised Approved Current Budget	February-22 Est @ Comp	March-22 Est @ Comp	Net Contingency Balance		Budget Summary Notes
ACMA Replacement	\$ 28,300,000	\$ 37,570,155	\$ 37,570,155	\$ 37,570,155	\$ 902,000		Current contingency decreased by \$24k due to various closeout items.
AHS Title IX Compliance	\$ 2,000,000	\$ 3,453,433	\$ 3,453,433	\$ 3,453,433			Completed; Final Cost
Capital Center Improvements & Data Center	\$ 5,000,000	\$ 12,820,187	\$ 12,820,187	\$ 12,820,187			Completed; Final Cost
District-Wide ADA Compliance	\$ 2,000,000	\$ 1,523,777	\$ 1,523,777	\$ 1,523,777			Projects in Process; budget 52% complete
District-Wide Communication System	\$ 7,200,000	\$ 5,282,072	\$ 5,282,072	\$ 5,282,072			Completed; Final Cost
District-Wide Facility Repairs	\$ 98,000,000	\$ 120,973,719	\$ 120,973,719	\$ 121,275,785			
District-Wide HVAC Controls	\$ 800,000	\$ 800,000	\$ 800,000	\$ 800,000			Projects in Process; budget 33% complete
Domestic / Fire Line Separation	\$ 800,000	<i>(Budget moved to Facilities Repair)</i>					
Five Oaks MS Renovation & Expansion	\$ 21,100,000	\$ 28,426,419	\$ 28,426,419	\$ 28,426,419	\$ 230,565		In Close-Out; Post-warranty work ongoing
Green Energy Technology	\$ 5,000,000	<i>(Budget Moved to Other Projects)</i>					Scope completed via new schools and rebuilds
Hazeldale K-5 Replacement	\$ 24,600,000	\$ 31,504,877	\$ 31,504,877	\$ 31,504,877			Completed; Final Cost
IT Data Center @ Capital Center	\$ 2,900,000	<i>(Budget Moved to CC Project)</i>					Scope completed via Capital Center Improvements
Kitchen Improvements	\$ 800,000	\$ 977,120	\$ 977,120	\$ 977,120			Projects in Process; budget 35% complete
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000	\$ 7,772,659	\$ 7,772,659	\$ 7,772,659			Completed; Final Cost
Maintenance Facility Improvements Phase I	\$ 10,000,000	\$ 11,263,990	\$ 11,263,990	\$ 11,263,990	\$ 19,511		
McKay ADA Improvements	\$ 400,000	\$ 634,540	\$ 634,540	\$ 634,540			Completed; Final Cost
New HS: Mountainside	\$ 109,000,000	\$ 184,135,294	\$ 184,135,294	\$ 184,135,294	\$ 43,204		In Close-Out; Post-warranty work ongoing
New ES: Sato K5	\$ 25,000,000	\$ 38,097,642	\$ 38,097,642	\$ 38,097,642			Completed; Final Cost
New MS: Tumwater	\$ 51,600,000	\$ 61,691,096	\$ 61,691,096	\$ 61,691,096			Construction completed 2016; Final outfitting ongoing
Raleigh Hills K-8 Improvements	\$ 9,700,000	\$ 1,419,490	\$ 1,419,490	\$ 1,419,490			Completed; Final Cost
Raleigh Hills K-8 Conceptual Design	\$ -	\$ 1,000,000	\$ 1,000,000	\$ 1,000,000	\$ 100,000	11.1%	
Raleigh Hills K-8 Improvements (Funding Hold)	\$ -	\$ 10,821,753	\$ 10,821,753	\$ 10,821,753			
Security Upgrades	\$ 10,000,000	\$ 18,458,530	\$ 18,458,530	\$ 18,458,530			Projects in Process; budget 96% complete
Seismic Upgrades	\$ 4,200,000	\$ 26,444,965	\$ 26,444,965	\$ 26,197,692			

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Project List	Original Budget Allocations	Revised Approved Current Budget	February-22 Est @ Comp	March-22 Est @ Comp	Net Contingency Balance		Budget Summary Notes
SHS Title IX Compliance	\$ 2,000,000	\$ 4,285,317	\$ 4,285,317	\$ 4,285,317			Completed; Final Cost
Springville K-8 Improvements	\$ 2,000,000	\$ 510,016	\$ 510,016	\$ 510,016			Completed; Final Cost
Vose K-5 Replacement	\$ 24,800,000	\$ 33,846,280	\$ 33,846,280	\$ 33,846,280			Completed; Final Cost
William Walker K-5 Replacement	\$ 24,600,000	\$ 34,626,711	\$ 34,626,711	\$ 34,626,711			Completed; Final Cost
Added Projects	\$ -	\$ 12,491,010	\$ 12,491,010	\$ 12,491,010			
Program Contingency	\$ 45,400,000						
Program Inflation	\$ 52,800,000						
Pre-Bond Expenditure Reimbursements	\$ 1,000,000	\$ 998,828	\$ 998,828	\$ 998,828			Completed; Final Cost
Bond Management Costs	\$ 20,000,000	\$ 30,990,506	\$ 30,990,506	\$ 30,990,506			
Bond Issuance Costs	\$ 6,000,000	\$ 4,000,000	\$ 4,000,000	\$ 4,000,000			
Construction Subtotal	\$ 600,000,000	\$ 726,820,386	\$ 726,820,386	\$ 726,875,179	\$ 1,295,280		
Learning Technology	\$ 56,000,000	\$ 56,000,000	\$ 56,000,000	\$ 56,000,000			
Critical Equipment	\$ 24,000,000	\$ 24,000,000	\$ 24,000,000	\$ 24,000,000			
Tech & Equip Subtotal	\$ 80,000,000	\$ 80,000,000	\$ 80,000,000	\$ 80,000,000			
Grand Totals	\$ 680,000,000	\$ 806,820,386	\$ 806,820,386	\$ 806,875,179	\$ 1,295,280		Contingency Balance change of -24K
Added Funding to Bond Program							
Bond Premium (First Bond Sale)	\$ 63,295,961						
Bond Premium (Second Bond Sale)	\$ 30,270,107						
Interest Earnings (First Bond Sale)	\$ 5,340,214						
Interest Earnings (Second Bond Sale)	\$ 13,236,261						
Other Additional Funding (see Tab)	\$ 16,034,445						
Grand Total Added Funding	\$ 128,176,988						
GRAND TOTAL 2014 BOND FUNDING	\$ 808,176,988						Total Funding increased \$303,622
Program Reserve		\$ 1,301,809					Program Reserve increased \$248,829
Program Reserve + Project Contingencies					\$ 2,597,089		Change of \$208,860

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Source	Funding	Assigned to Projects	Assigned to Program Reserve	Budget Summary Notes
Remaining 2006 Bond Savings	\$ 576,615	Mountainside HS	\$ -	
Capital Center Rent Revenue Balance	\$ 433,385	Mountainside HS	\$ -	
Construction Excise Tax Revenue	\$ 1,130,655	Capital Center	\$ -	
Construction Excise Tax Revenue forecasted to 2021	\$ 5,021,577		\$5,021,577	
THPRD reimb.	\$ 449,783		\$ 449,783	
SB 1149 reimb.	\$ 3,264,390	District-wide Repairs	\$ 248,828	
ETO reimb.	\$ 1,630,532	District-wide Repairs	\$ 1,443,453	
Facility grants	\$ 3,027,507		\$ 3,027,507	
Sato: TVWD Reimbursement	\$ 500,000	Sato K-5	\$ -	
TOTAL	\$16,034,445		\$10,191,148	

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Added Projects	Approved by & Date	Original Budget	Revised Approved Current Budget	February-22 Est @ Comp	March-22 Est @ Comp	Net Contingency Balance	Budget Summary Notes
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$ 99,368	\$ 99,368	\$ 99,368	\$ -	Completed; Final Cost
Portable Relocations 2014	Sr LT 5/20/14		\$ 591,685	\$ 591,685	\$ 591,685	\$ -	Completed; Final Cost
Portable Relocations 2015	Sr LT 3/2015		\$ 294,257	\$ 294,257	\$ 294,257	\$ -	Completed; Final Cost
Title IX Projects - Group II	Sr LT 3/2015		\$ 1,030,697	\$ 1,030,697	\$ 1,030,697	\$ -	Completed; Final Cost
Classroom Door Locks	SB 6/18/18		\$ 2,179,293	\$ 2,179,293	\$ 2,179,293	\$ -	Budget 85% complete; phase 2 work ongoing
Security Upgrades: Classroom Walls	SB 6/15/20		\$ 2,045,710	\$ 2,045,710	\$ 2,045,710	0.0%	
Security Upgrades: Paging	SB 6/15/20		\$ 500,000	\$ 500,000	\$ 500,000	\$ -	
Security Upgrades: Site Fencing	SB 6/21/21		\$ 1,700,000	\$ 1,700,000	\$ 1,700,000	\$ -	
Vose Classroom Addition	SB 6/21/21		\$ 3,900,000	\$ 3,900,000	\$ 3,900,000	0.0%	Transferred \$150K to Sato Classroom
Sato Classroom Addition	SB 2/28/22		\$ 150,000	\$ 150,000	\$ 150,000		Design approved at 2/28/22 SB Meeting.
Added Projects Total		\$ -	\$ 12,491,010	\$ 12,491,010	\$ 12,491,010		

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Project	Initial Budget	Revised Approved Current Budget	February-22 Est @ Comp	March-22 Est @ Comp	Net Contingency Balance	Budget Summary Notes
Completed Projects	\$ 27,832,905	\$ 59,421,061	\$ 59,421,061	\$ 59,421,061		Completed; Final Cost
Projects in Close-out	\$ 6,883,538	\$ 21,605,377	\$ 21,605,377	\$ 21,605,377	\$ 545,097 2.6%	
2022 Repipes	\$ -	\$ 1,500,000	\$ 1,500,000	\$ 1,500,000		0.0%
2021 Roof Replacements	\$ 1,972,000	\$ 5,100,797	\$ 5,100,797	\$ 5,100,797		0.0%
Hiteon HVAC Controls Upgrade	\$ 200,000	\$ 563,783	\$ 563,783	\$ 563,783	\$ -	0.0%
Raleigh Park Sewer	\$ 47,000	\$ 250,000	\$ 250,000	\$ 250,000		0.0%
ISB HVAC & Roof	\$ 864,000	\$ 2,266,112	\$ 2,266,112	\$ 2,712,112		0.0%
District-Wide Fire Alarm Resiliency	\$ 1,303,000	\$ 2,474,120	\$ 2,474,120	\$ 2,474,120	\$ -	0.0%
2022 Roof Replacements Group 1	\$ 1,380,000	\$ 3,076,000	\$ 3,076,000	\$ 3,323,273		0.0%
2022 Roof Replacements Group 2	\$ 277,000	\$ 615,000	\$ 2,665,152	\$ 2,665,152		0.0%
2022 HVAC Upgrades Group 1	\$ 882,000	\$ 2,291,380	\$ 2,291,380	\$ 2,291,380		0.0%
Five Oaks Roof	\$ -	\$ 150,000	\$ 150,000	\$ 150,000	\$ -	0.0%
New Schools Post-Warranty Fund	\$ -	\$ 650,000	\$ 650,000	\$ 650,000		
Maint Dept Repair & Improvement Projects*	\$ 9,068,708	\$ 9,068,708	\$ 9,068,708	\$ 10,439,322		
Repair Projects Total	\$ 50,710,151	\$ 109,032,338	\$ 111,082,490	\$ 113,146,377		
Repair Program Balance Available	\$ 47,289,849	\$ 12,243,447	\$ 10,193,295	\$ 8,129,409		
Repair Program EAC Balance	\$ -	\$ -				
Repair Program Budget (Less Transfers In/Out)	\$ 98,000,000	\$ 121,275,785	\$ 121,275,785	\$ 121,275,785		
*Budget and Est @ Comp. will increase each month as additional Maintenance Dept. managed Repair Projects are scheduled.						
Transfer Tracking						
Initial Budget	\$ 98,000,000					
Previous Transfers	\$ 5,544,581					
SB 1149 Reimbursements	\$ 3,015,562					
ETO Reimbursements	\$ 187,079					
Additional Funding - Chehalem Repipe - Approved 6.15.2020	\$ 500,000					
Additional Funding - McKinley Repipe - Approved 6.15.2020	\$ 500,000					
Additional Funding - Post Warranty Fund - Approved 1.28.2021	\$ 500,000					
Additional Funding - Budget Increase - Approved 3.15.2021	\$ 14,070,000					
Funds Transferred from Domestic Fire/ Line Separation	\$ 977,120					
Funds transferred to Seismic- Bethany ES	\$ (2,230,000)					
Funds transferred to Added Projects - Classroom Door Locks	\$ (179,293)					
Additional Funding - Elmonica Repipe - Approved 6.21.2021	\$ 500,000					
Funds transferred to Added Projects - Classroom Walls	\$ (45,710)					
Funds transferred from Five Oaks	\$ 150,000					
Funds transferred to Seismic- West TV ES	\$ (460,827)					
Transfer from Seismic for Roof Repl - Group 1	\$ 247,273					
Balance	\$ 121,275,785					

2014 Bond Program Financial Status Report

Financial Summary

Data as of March 31, 2022

Seismic Projects	Original Budget	Revised Approved Current Budget	February-22 Est @ Comp	March-22 Est @ Comp	Net Contingency Balance	Budget Summary Notes
A/E Scoping/Surveys	\$ -	\$ 222,058	\$ 222,058	\$ 222,058		Completed; Final Cost
Aloha HS	\$ 1,732,898	\$ 18,138,738	\$ 18,138,738	\$ 18,138,738		
Beaver Acres ES	\$ 1,714,444	\$ 5,926,866	\$ 5,926,866	\$ 5,926,866		Completed; Final Cost
Beaverton HS	\$ 246,184	(Budget Transferred to Seismic Program) (Budget Moved to Facility Repairs)				Scope completed via BHS Gym Ceiling project
Cedar Mill ES	\$ 144,771					Scope completed via Cedar Mill Roof & HVAC project
Cooper Mt. ES	\$ 361,703	\$ 3,063,556	\$ 3,063,556	\$ 3,063,556	0.0%	
Bethany ES	\$ -	\$ 4,930,811	\$ 4,930,811	\$ 4,930,811	0.0%	
Seismic Red Zones	\$ -	\$ 160,300	\$ 160,300	\$ 160,300		
2022 SRGP Planning	\$ -	\$ 100,000	\$ 100,000	\$ 100,000		
West TV Seismic (Gym)	\$ -	\$ 597,827	\$ 597,827	\$ 597,827	0.0%	
Seismic Red Zones (Rock Creek/SHS)	\$ -			\$ 208,928		Project in Planning for 2022; Budget allocated from the Seismic Funding Hold
Seismic Funding Hold	\$ -	\$ 568,095	\$ 568,095	\$ 111,894		
(Projects Financially Complete)						
Seismic Projects Total	\$ 4,200,000	\$ 33,708,251	\$ 33,708,251	\$ 33,460,978		
TAPS Seismic Grant	\$ -	\$ (22,545)	\$ (22,545)	\$ (22,545)		
AHS Seismic Rehabilitation Grant	\$ -	\$ (2,500,000)	\$ (2,500,000)	\$ (2,500,000)		
Beaver Acres Seismic Rehabilitation Grant	\$ -	\$ (2,500,000)	\$ (2,500,000)	\$ (2,500,000)		
Cooper Mnt Seismic Rehabilitation Grant	\$ -	\$ (2,240,741)	\$ (2,240,741)	\$ (2,240,741)		
Seismic Program Bond Cost Balance	\$ 4,200,000	\$ 26,444,965	\$ 26,444,965	\$ 26,197,692		
Seismic Program Less Transfers In/Out	\$ 26,197,692					
Transfer Tracking						
Initial Budget	\$ 4,200,000					
Program Escalation	\$ 1,006,740					
AHS Roofing - From Facility Repairs	\$ 575,193					
Beaver Acres Roofing - From Facility Repairs	\$ 1,138,000					
AHS Roofing - Balance From Facility Repairs	\$ 3,477,807					
Program Reserve - Approved by School Board 6.18.18	\$ 5,450,000					
Transfer to Facility Repairs - Cedar Mill	\$ (166,052)					
Cooper Mnt Roofing - From Facility Repairs	\$ 128,000					
Program Reserve - Approved by School Board 10.28.19	\$ 6,849,950					
Beaver Acres Windows - From Facility Repairs	\$ 605,000					
Beaver Acres Re-pipe - From Facility Repairs	\$ 489,500					
Bethany Roof and HVAC Seismic Transfer	\$ 2,230,000					
West TV Seismic (Gym) Transfer	\$ 460,827					
Transfer to McKinley Roofing (2022 Roof Phase 1)	\$ (247,273)					
Balance	\$ 26,197,692					

**2014 Bond Program Learning Technology/Classroom Systems
and Critical Equipment Purchases
March 31, 2022**

Data as of March 31, 2022

Learning Technology/Classroom Systems (\$56 Million)						
Project Name	Total Budget Project	% Complete	Project To Date Expenditures	2021-22 Budget	2021-22 Expenditures as of 3/31/22	Annual Description of Expenditures
Networking Upgrades	\$ 11,542,526	70%	\$ 8,095,250	\$ 5,181,920	\$ 1,734,644	Maintaining current wired and wireless networking capacity and addressing areas of need. Data Center server hardware expanded and replaced. New staff and departmental storage implemented. Replacement of school switch project started at elementary schools.
Digital Curriculum Development	\$ 5,286,785	96%	\$ 5,053,722	\$ 698,711	\$ 465,648	Salary to maintain five digital curriculum specialists. Digital Curriculum Specialists are responsible for curating and developing high quality digital curriculum and materials that align to our Standards Based Learning System. This team was a valuable resource last spring when we were pressed to provide additional resources for district teachers during the COVID-19 remote learning implementation.
Future Ready Schools	\$ 29,496,360	99.6%	\$ 29,383,599	\$ 202,361	\$ 89,599	Two rounds of student devices were purchased from the bond. Monies remaining in the Future Ready budget are partially funding hardware repair staff focused on repairing our fleet of over 50,000 iPad and Chromebook devices.
Technology Modernization	\$ 2,909,823	83%	\$ 2,426,302	\$ 560,182	\$ 76,661	Continued Business Continuity Plan (BCP) updates. Continued pilot of classrooms and conference room technology solutions for remote work. Upgrades to HR Center and the BusinessPlus ERP system.
Other Technology/Curriculum Projects	\$ 6,764,506	100%	\$ 6,764,506	\$ -	\$ -	Completed Technology/Curriculum Projects. Includes: student laptop replacements in 2014-15, high school science technology in 2015-16, positive change grants 2014-15 through 2016-17.
Learning Technology/ Classroom Systems Total	\$ 56,000,000	92%	\$ 51,723,378	\$ 6,643,174	\$ 2,366,552	

**2014 Bond Program Learning Technology/Classroom Systems
and Critical Equipment Purchases
March 31, 2022**

Data as of March 31, 2022

Critical Equipment (\$24 Million)						
Project Name	Total Budget Project	% Complete	Project To Date Expenditures	2021-22 Budget	2021-22 Expenditures as of 3/31/22	Annual Description of Expenditures
Copiers	\$ 1,945,124	86%	\$ 1,668,284	\$ 300,000	\$ 23,159	Approximately \$300,000/year over eight years.
Athletic Equipment	\$ 1,021,737	93%	\$ 945,685	\$ 278,982	\$ 202,929	Approximately \$100,000/year over three years beginning in year 2. \$75,970 was transferred in year 2 to the Scoreboard Replacements Project. An additional \$800,000 will be split over years six through eight.
Maintenance Equipment	\$ 2,289,219	73%	\$ 1,680,103	\$ 843,784	\$ 234,668	Approximately \$120,000/year over four years beginning in year 2. Year 2 will have \$185,000. An additional \$1.7 million will be split over the final three years of the bond, beginning in year six.
Early Learning Playground Equipment	\$ 15,366	96%	\$ 14,713	\$ 6,000	\$ 5,347	Playground equipment for Early Learning program at seven elementary schools.
Flex Devices	\$ 36,500	92%	\$ 33,616	\$ 36,500	\$ 33,616	5 iMacs, 5 MacBook Pros, 11 iPads with pencils and keyboards, and 11 Dell monitors for Flex in December 2021
Other Equipment Purchases	\$ 18,692,054	98%	\$ 18,318,463	\$ -	\$ -	Other critical equipment purchases as needed. Purchase of \$15,000 towards new locker banks at Stoller in 14-15, \$250,000 towards new musical instruments in 14-15 and 15-16, \$184,050 for cafeteria table replacements in 15-16, \$1,397,733 for classroom furniture for full day kindergarten in 2015-16, \$344,973 for high school scoreboard replacements in 2015-16 and 2016-17, \$121,066 towards BSD's portion of shock pad installation at SW Quadrant Park with THPRD in 2016-17 and InTouch Printers in 2018. The District purchased \$16M in buses over the first 7 years of the bond. All are included in this line.
Critical Equipment Total	\$ 24,000,000	94%	\$ 22,660,864	\$ 1,465,266	\$ 499,719	
Grand Total	\$ 80,000,000	93%	\$ 74,384,241	\$ 8,108,440	\$ 2,866,271	
Total Bond Funds Remaining	\$ 5,615,759					

