


Bond Program Status Report

Through May 2018

2014 Bond Program Executive Summary

May 2018

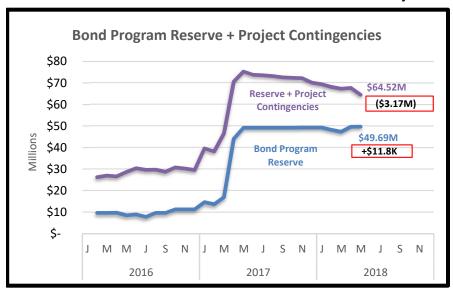

Bond Program Reserve = Funding available to the Bond Program but not yet allocated to a project Project Contingencies = Funding contained within an approved project budget

Bond Program Funding Total		\$ 802,276,993
Revised Approved Current Budget	-	\$ 752,590,539
Bond Program Reserve		\$ 49,686,454
Bond Program Reserve		\$ 49,686,454
Net Contingency Balance	+	\$ 14,833,421
		\$ 64,519,875
May 2018, Program Estimate at Complete (EAC)		\$ 787,058,836
Projected Program Reserve Estimate at Complete		\$ 15,218,157

Overall Program Perspective

Hazeldale is progressing well and remains several weeks ahead of where Vose was at this time last year.

Financial forecasts for Five Oaks and ACMA have moved them to the watch list due to large forecasted contingency decreases. However, both project teams are working to mitigate cost events and the long-term outlook for both projects remains positive.

MWSDVE Participation:

Consultants: 10%; Contractors: 12.2%; Apprenticeship: 20%

Budget Perspective

This month the overall Program Reserve increased by \$11.8K, while the Reserve + Project Contingencies decreased by \$3.17M. All projects remain within their current approved budgets. Primary cost events were:


- ACMA's forecasted contingency decrease of \$1.96M is based on the latest Schematic Design estimate. Staff is mitigating costs by reducing finishes, glazing, and site work, and we should see a more favorable Design Development estimate in late June.
- Mountainside's forecasted contingency decrease of \$806K reflects the forecasted final reconciliation of contractor and owner cost logs.
- BHS Gym Ceiling and Truss Repair's forecasted contingency decrease
 of \$173K is an updated projected cost of additional shoring and truss
 repair work for damaged areas discovered after bids.
- Five Oak's forecasted contingency decrease of \$134K is due to costs needed to relocate portables and those associated with moving to Timberland.
- William Walker's forecasted contingency drop of \$228K is due to additional jurisdictional requirements and revisions to the utility configuration.

Schedule Perspective

- · Work at Hazeldale is progressing on schedule.
- Five Oaks Construction Documents complete, bidding is underway.
 Expect to receive GMP proposal for approval at July School Board meeting.
- Early work at William Walker has begun. Mass grading on the access road is scheduled to start 6/11. Permitting delays are becoming a concern, but staff continues to press through issues.
- Neighborhood meeting for ACMA scheduled for mid-June.
- · Work has begun at the BHS Gym Ceiling and Truss Repair project.


School Bond Program 2018 Activity Map



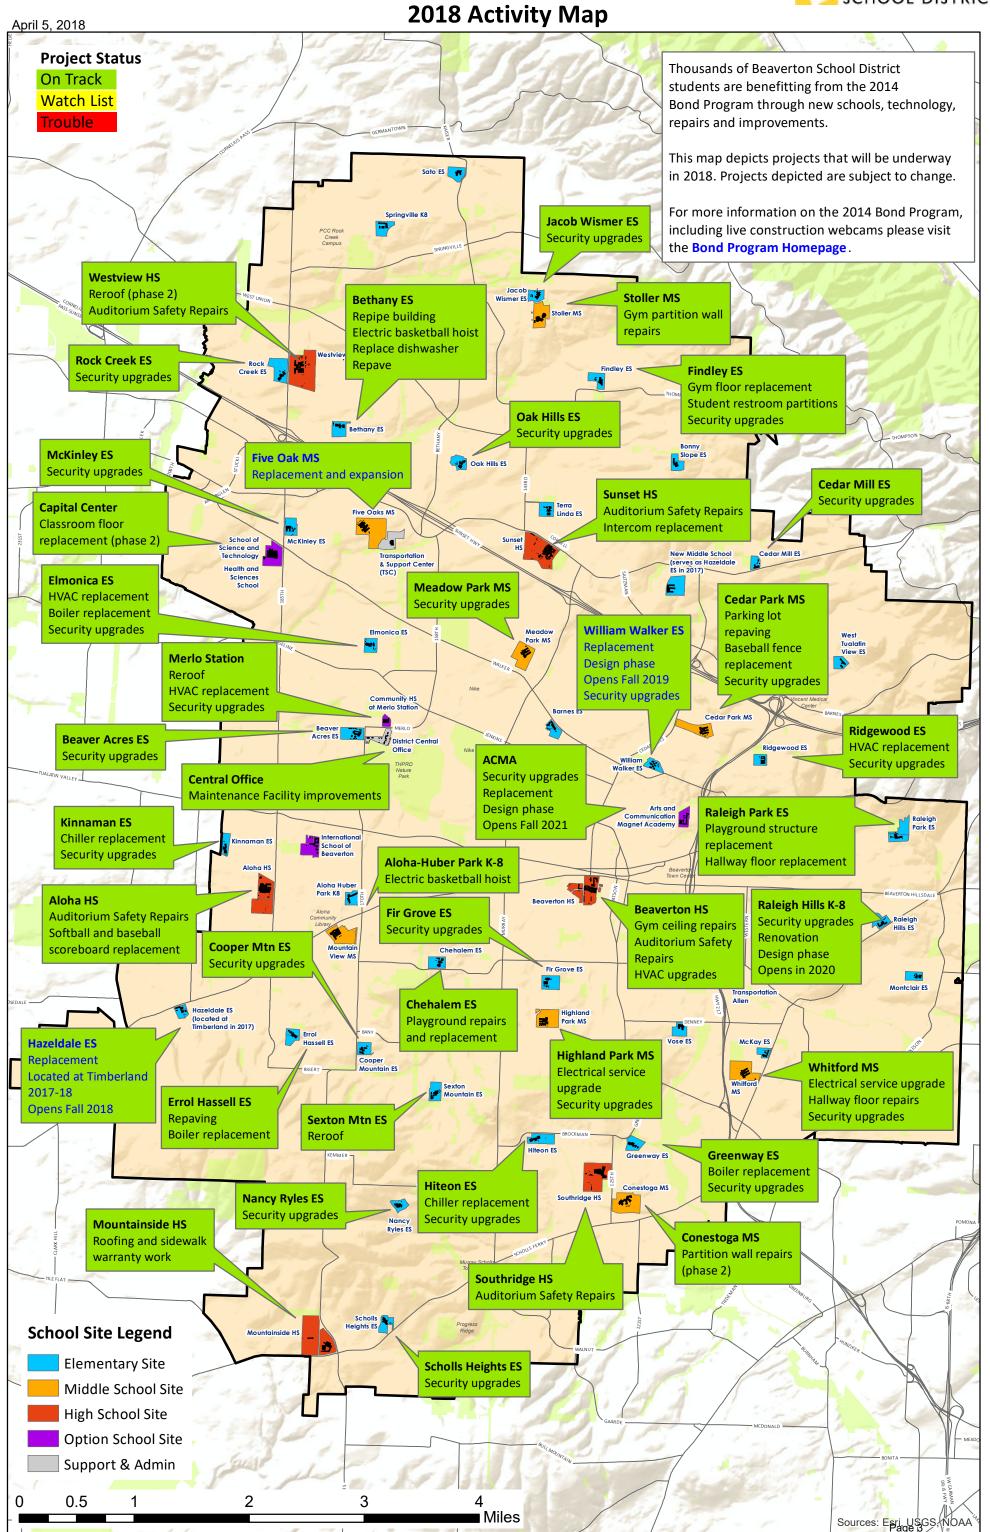


2014 Bond Construction Program

Overall Performance May 2018 Report

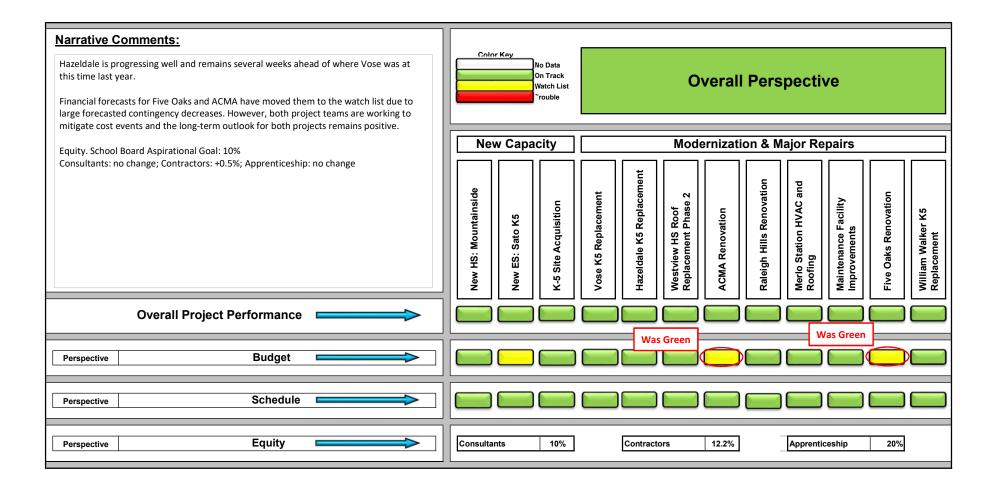


2014 Bond Construction Program

Budget Perspective May 2018 Report

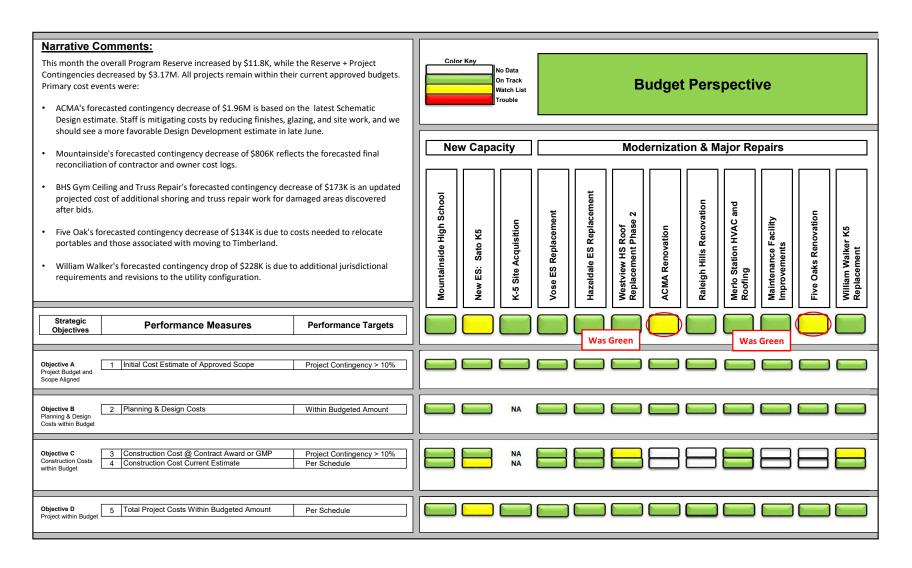


2014 Bond Construction Program

Schedule Perspective May 2018 Report

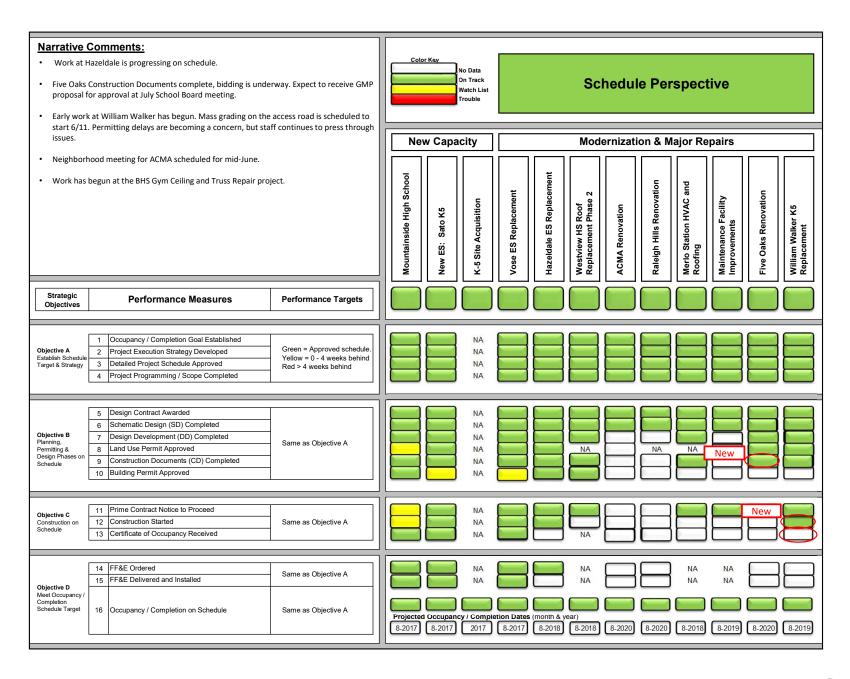


2014 Construction Bond Program

Equity Performance May 2018 Report

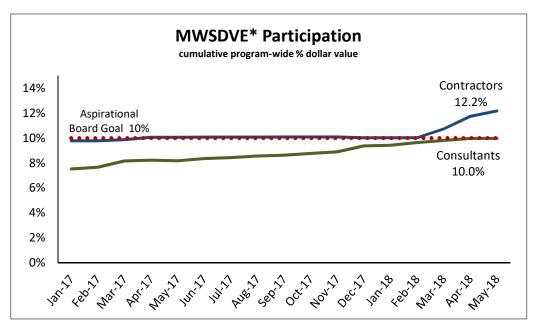

^{*}Minority, Women and Service Disabled Veteran Owned Enterprises

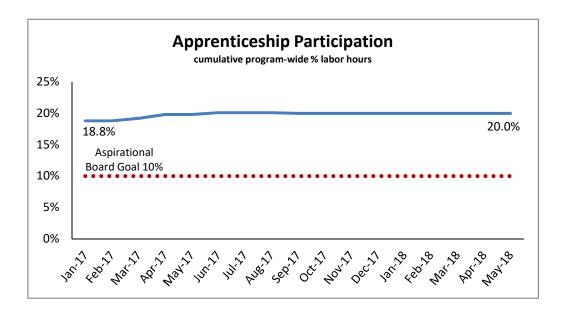

Overall Program Cost Forecast and Available Funding

Project List	Original Funding Allocations	Funding Increases Available to Bond Program	Update	ruction Cost s & Escalated · Inflation			
ACMA Replacement	\$ 28,300,000		\$	39,432,555	SD estimate 2018		
AHS Title IX Compliance	\$ 2,000,000		\$	3,697,441	(eB 5/31/18 EAC)	Color Key	
Capital Center Improvements & Data Center	\$ 5,000,000		\$	12,820,187	Completed	Final Cost Estimate	1
District-Wide ADA Compliance	\$ 2,000,000		\$	2,000,000		Fixed Cost	
District-Wide Communication System	\$ 7,200,000		\$	5,518,030	(eB 5/31/18 EAC)	Estimate Update	(Based upon on-going work)
District-Wide Facility Repairs	\$ 98,000,000		\$	98,135,296		Inflation Projection	(Prior to work starting)
District-Wide HVAC Controls	\$ 800,000		\$	800,000		Abbreviations:	RLB = Rider Levett Bucknall
Domestic / Fire Line Separation	\$ 800,000		\$	977,120			eB = eBuilder proj. mgmt info system
Five Oaks MS Renovation & Expansion	\$ 21,100,000		\$	27,501,419	Schematic Design B	Est Update 3/2017	EAC = \$ Estimate at proj. completion
Green Energy Technology	\$ 5,000,000		\$	-			
Hazeldale K-5 Replacement	\$ 24,600,000		\$	34,256,091	(eB 5/31/18 EAC)		
IT Data Center @ Capital Center	\$ 2,900,000			Moved to CC Project)			
Kitchen Improvements	\$ 800,000		\$	977,120			
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000		\$	7,800,000	School Board Appro	oved \$2.3M increase,	5/15/17
Maintenance Facility Improvements	\$ 10,000,000		\$	11,263,990	Schematic Design B	Estimate 1/2017	
McKay ADA Improvements	\$ 400,000		\$	634,540	Completed		
New HS: Mountainside	\$ 109,000,000		\$	184,735,294	(eB 5/31/18 EAC)		
New ES: Sato K-5	\$ 25,000,000		\$	38,575,000	(eB 5/31/18 EAC)		
New MS @ Timberland	\$ 51,600,000		\$	61,371,096	(eB 5/31/18 EAC)		
Raleigh Hills K-8 Improvements	\$ 9,700,000		\$	13,241,243	Schematic Design B	Estimate 1/2017	
Security Upgrades	\$ 10,000,000		\$	10,600,000			
Seismic Upgrades	\$ 4,200,000		\$	5,781,933			

Overall Program Cost Forecast and Available Funding

Project List	Original Funding Allocations	Avai	ding Increases ilable to Bond Program		onstruction Cost dates & Escalated for Inflation	
SHS Title IX Compliance	\$ 2,000,000			\$	4,285,317	Completed
Springville K-8 Improvements	\$ 2,000,000			\$	510,016	Completed
Vose K-5 Replacement	\$ 24,800,000			\$	33,977,390	(eB 5/31/18 EAC)
William Walker K-5 Replacement	\$ 24,600,000			\$	36,684,200	(eB 5/31/18 EAC)
Added Projects	\$ -			\$	2,016,433	
Program Contingency	\$ 45,400,000			F	unding available	
Program Inflation	\$ 52,800,000				(not a cost)	
Pre-Bond Expenditure Reimbursements	\$ 1,000,000			\$	998,828	
Bond Management Costs	\$ 20,000,000			\$	30,000,000	
Bond Issuance Costs	\$ 6,000,000			\$	4,000,000	
Construction	\$ 600,000,000			\$	672,590,539	
Learning Technology	\$ 56,000,000			\$	56,000,000	
Critical Equipment	\$ 24,000,000			\$	24,000,000	
Fech & Equip Subtotal	\$ 80,000,000			\$	80,000,000	
Fotal Original Funding	\$ 680,000,000					
Total Cost Projection				\$	752,590,539	
Bond Premium 1st Bond Sale		\$	63,295,961			
Bond Premium 2nd Bond Sale		\$	30,270,107			
Interest Earnings 1st Bond Sale		\$	5,200,000			
Interest Earnings 2nd Bond Sale		\$	9,539,685		l	
Other Additional Funding (see tab)		\$	13,971,240		l	
Additional Funding Subtotal		\$	122,276,993		l	
Total Funding Available		\$ 8	802,276,993			
Total Cost Updates				\$	752,590,539	+11.8K
Funding Balance Vs. Cost Updates						\$ 49,686,454 Program Reserve

Project List	Original Budget	Added Funding to		Approved		Apr-18		May-18	Net Con	tingency Balance
i roject List	Allocations	Bond Program	Currer	nt Budget	Budget Est @ Comp.		Е	st @ Comp.	\$	%
ACMA Replacement	\$ 28,300,000		\$	(\$1.96M) A	Additio	onal site	٦	39,432,555	\$ 2,690,489	7.3%
AHS Title IX Compliance	\$ 2,000,000		\$			nd construction mate; staff		3,697,441	\$ 234,181	6.8%
Capital Center Improvements & Data Center	\$ 5,000,000		\$	mitigating (costs	by reducing		12,820,187	Compl	eted; Final Cost
District-Wide ADA Compliance	\$ 2,000,000		\$	finishes, gla	azing	and site work.		2,000,000		
District-Wide Communication System	\$ 7,200,000		\$	5,518,030	\$	5,518,030	\$	5,518,030	\$ -	
District-Wide Facility Repairs	\$ 98,000,000		\$	98,135,296	\$	122,970,751	\$	122,970,751	(\$12.410)	Doutoble veloceticus
District-Wide HVAC Controls	\$ 800,000		\$	800,000	\$	800,000	\$	800,000	moving (Portable relocation; costs
Domestic / Fire Line Separation	\$ 800,000		\$	977,120	\$	977,120	\$	977,120		
Five Oaks MS Renovation & Expansion	\$ 21,100,000		\$	27,501,419	\$	27,501,419	\$	27,501,419	\$ 1,640,563	6.3%
Green Energy Technology	\$ 5,000,000			t Moved to Projects)						
Hazeldale K-5 Replacement	\$ 24,600,000		\$	34,256,091	\$	34,256,091	\$	34,256,091	\$ 2,242,337	7.0%
IT Data Center @ Capital Center	\$ 2,900,000			t Moved to Project)						
Kitchen Improvements	\$ 800,000		\$	977,120	\$	977,120	\$	977,120		
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000		\$	7,800,000	\$	7,800,000	\$	7,800,000	\$ 16,590	0.2%
Maintenance Facility Improvements Phase-1	\$ 10,000,000		\$	11,263,990	\$	11,263,990	\$	11,263,990	\$ 1,717,359	18.0%
McKay ADA Improvements	\$ 400,000		\$			asted final of contractor		634,540	Compl	eted; Final Cost
New HS: Mountainside	\$ 109,000,000		\$ 1	84 and own				184,735,294	\$ 750,000	0.4%
New ES: Sato K5	\$ 25,000,000		\$	38,575,000	\$	38,575,000	\$	38,575,000	\$ 54,300	0.1%
New MS @ Timberland	\$ 51,600,000		\$	61,371,096	\$	61,371,096	\$	61,371,096	\$ 266,115	0.4%
Raleigh Hills K-8 Improvements	\$ 9,700,000		\$	13,241,243	\$	13,241,243	\$	13,241,243	\$ 2,048,129	18.3%
Security Upgrades	\$ 10,000,000		\$	10,600,000	\$	14,487,387	\$	14,487,387		
Seismic Upgrades	\$ 4,200,000		\$	5,781,933	\$	11,527,388	\$	11,527,388		

Project List	o	riginal Budget		Ided Funding to		vised Approved		Apr-18	May-18		Net Con	tingency Balance
1 Toject List		Allocations		Bond Program	C	urrent Budget		Est @ Comp.	Est @ Comp.		\$	%
SHS Title IX Compliance	\$	2,000,000			\$	4 285 317		4 285 317	\$ 4,285,317		Compl	eted; Final Cost
Springville K-8 Improvements	\$	2,000,000			\$	(\$228K) Additi requirements;		,	\$ 510,016	Completed; Final Cost		
Vose K-5 Replacement	\$	24,800,000			\$	configuration		· '	\$ 33,977,390	\$	141,862	0.4%
William Walker K-5 Replacement	\$	24,600,000			\$	36,684,200	\$	36,684,200	\$ 36,684,200	\$	3,031,496	9.0%
Added Projects					\$	2,016,433	\$	2,025,736	\$ 2,016,433			
Program Contingency	\$	45,400,000										
Program Inflation	\$	52,800,000										
Pre-Bond Expenditure Reimbursements	\$	1,000,000			\$	998,828	\$	998,828	\$ 998,828		Compl	eted; Final Cost
Bond Management Costs	\$	20,000,000			\$	30,000,000	\$	30,000,000	\$ 30,000,000			
Bond Issuance Costs	\$	6,000,000			\$	4,000,000	\$	4,000,000	\$ 4,000,000			
Construction	\$	600,000,000			\$	672,590,539	\$	707,068,139	\$ 707,058,836			
Learning Technology	\$	56,000,000			\$	56,000,000	\$	56,000,000	\$ 56,000,000			
Critical Equipment	\$	24,000,000			\$	24,000,000		24,000,000	24,000,000			
Tech & Equip Subtotal	\$	80,000,000			\$	80,000,000	\$	80,000,000	\$ 80,000,000			
Grand Totals	\$	680,000,000			\$	752,590,539	\$	787,068,139	\$ 787,058,836	\$	14,833,421	
Bond Premium			\$	93,566,068								
Interest Earnings			\$	14,739,685								
Other Additional Funding (see Tab)			\$	13,971,240								
Other Added Funding			\$	122,276,993								
						111.04	1					
GRAND TOTAL 2014 BOND FUNDING			\$	802,276,993		+11.8K	ل					(\$3.17M)
Program Reserve					\$	49,686,454	\$	15,208,854	\$ 15,218,157			(33.17101)
Program Reserve + Project Contingencies												\$ 64,519,8

2014 Bond Program Financial Status Report

Additional Funding Allocations

Additional Funding Allocations to Bond Program										
Source		Funding	Assigned to Projects		ssigned to ram Reserve					
Remaining 2006 Bond Savings	\$	576,615	Mountainside HS							
Capital Center Rent Revenue Balance	\$	433,385	Mountainside HS							
Construction Excise Tax Revenue	\$	1,130,655	Capital Center							
Construction Excise Tax Revenue forecasted to 2021	\$	5,321,577	·		\$6,462,036					
THPRD reimb.	\$	449,783		\$	449,783					
SB 1149 reimb.	\$	1,734,435	District-wide Repairs							
ETO reimb.	\$	797,283	District-wide Repairs	\$	778,341					
Facility grants	\$	3,027,507		\$	1,887,048					
Sato: TVWD Reimbursement	\$	500,000	Sato K-5							
TOTAL		\$13,971,240			\$9,577,208					

2014 Bond Program Financial Status Report Added Projects

Added Projects	Approved by	Original Budget		sed Approved		Mar-18		Apr-18	Net	Cont Bala	ingency nce
	& Date	o o	Cur	rent Budget	E	Est @ Comp.		st @ Comp.	\$		%
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$	99,368	\$	99,368	\$	99,368		Comp	eted
Portable Relocations 2014	Sr LT 5/20/14		\$	592,111	\$	592,111	\$	592,111		Comp	eted
Portable Relocations 2015	Sr LT 3/2015		\$	294,257	\$	294,257	\$	294,257		Comp	eted
Title IX Projects - Group II	Sr LT 3/2015		\$	1,030,697	\$	1,040,000	\$	1,030,697		Comp	eted
(Projects Financially Complete)											
Added Projects Total		\$ -	\$	2,016,433	\$	2,025,736	\$	2,016,433	\$	-	

2014 Bond Program Financial Status Report

District-Wide Repair Projects - Budget = \$98,000,000

Project	In	itial Budget	Rev	rised Approved		Ap	r-18		May-18	Net Contingency Balance			
Project		CA (Building Condition Assessment)	Cı	ırrent Budget			Comp.	Е	st @ Comp.		\$	%	
											·		
Completed Projects	\$	9,135,577	,135,577 \$ (\$173K) Updated projected 330				330,965	\$	20,330,965		Completed; Final (Cost	
Beaverton Gym Ceiling and Truss Repair	\$	117,392	\$	costs for addition and truss repair			438,410	\$	1,442,044	\$	(3,634)	-0.3%	
Beaverton HS HVAC	\$	3,900,000	\$	damaged areas			873,377	\$	3,873,377	\$	151,115	4.1%	
Conestoga Plumbing & Water Int Repair	\$	-	\$	after bids.			317,235	\$	3,317,235	\$	70,524	2.2%	
District-Wide Auditorium Upgrades	\$	4,384,538	\$	4,992,098	\$		6,563,549	\$	6,563,549				
HVAC (BCA) 2017	\$	1,090,624	\$	1,090,624	\$		1,090,624	\$	1,090,624				
WHS Roof Replacement Phase I & 2	\$	2,055,558	\$ _	1 176 673	2	_	4,476,673	\$	4,476,673	\$	396,493	9.7%	
Merlo Station HVAC and Roofing	\$	1,437,729		\$ (\$84K) PGE requested design changes to move 4,40			4,409,512	\$	4,409,512	\$	609,200	16.0%	
Ridgewood HVAC and Electrical	\$	829,173		building main dis		t	4,384,848	\$	4,384,848	\$	433,241	11.0%	
Sexton Mountain Roof	\$	619,878	\$	outside. 1,066,952				\$	1,066,952	\$	83,742	15.6%	
HP/Whitford Electrical	\$		Φ	646,000	ф	 1	616,000	\$	616,000	\$	20,000	3.4%	
Bethany Repipe	\$	Updated budget reflects most recent bid results. Costs reflect 1,200,000				\$	1,200,000	\$	94,758	8.6%			
Mountain View Roof	\$						\$	4,284,831	\$	100,000	8.7%		
Maint Dept Repair & Improvement Projects*	\$	5 will allo this Sun		to get the project	done		4,745,116	\$	5,336,301				
Repair Projects Total	\$	36,180,652	\$	57,330,920	\$	5	7,513,260	\$	62,392,911	\$	1,955,439		
Repair Program Balance Available	\$	61,819,348	\$	40,804,376	\$	4	0,622,036	\$	35,742,385				
Repair Program Less Transfers In/Out	\$	98.135.296											
Budget and Est @ Comp. will increase each month as addition	· ·	,,	mana	ged Repair Proje	cts are	schedu	ıled.						
Transfer Tracking													
SHS Repairs	\$	(1,881,416)											
SHS Emergency Elect	\$	745,833											
Capital Center Building Repairs	\$	(2,280,000)											
Capital Center Building Repairs	\$	1,090,725											
Transfer From District Wide Communications System	\$	81,970											
BB 1149 Reimbursements TO Reimbursements	\$	1,734,435 18,942											
Additional Funding for Bethany Repipe - Approved 2.6.18	\$	1,200,000											
AHS Roofing transferred to AHS Seismic	\$	(575,193)											
Net		135,296											
Balance	_		\$	98,135,296									

2014 Bond Program Financial Status Report Seismic Projects

Sojomio Projecto	Original Budget	Revised Approved			Apr-18		May-18	Net Contingency Balance			
Seismic Projects	Original Budget	Current Budget		E	st @ Comp.	E	st @ Comp.		\$	%	
									•		
A/E Scoping/Surveys	\$ -	\$ 193,895		\$	193,895	\$	193,895	\$	-	0.0%	
Aloha HS	\$ 1,732,898	\$ 2,652,769		\$	8,149,142	\$	8,149,142	\$	-	0.0%	
Beaver Acres ES	\$ 1,714,444	\$ 2,055,451		\$	4,159,316	\$	4,159,316	\$	-	0.0%	
Beaverton HS	\$ 246,184	\$ 287,635		\$	506,192	\$	506,192	\$	-	0.0%	
Cedar Mill ES	\$ 144,771	\$ 166,052		\$	297,672	\$	297,672	\$	-	0.0%	
Cooper Mt. ES	\$ 361,703	\$ 426,131		\$	743,716	\$	743,716	\$	-	0.0%	
(Projects Financially Complete)											
Seismic Projects Total	\$ 4,200,000	\$ 5,781,933		\$	14,049,933		14,049,933		-		
TAPS Seismic Grant		\$ (22,545)		\$	(22,545)		(22,545)				
AHS Seismic Rehabilitation Grant	-	\$ (2,500,000))	\$	(2,500,000)	\$	(2,500,000)				
Seismic Program Cost Balance				\$	11,527,388	\$	11,527,388				
Seismic Program Less Transfers In/Out	\$ 5,781,933										
Transfer Tracking											
Program Escalation	\$ 1,006,740										
AHS Roofing - From BCA	\$ 575,193										
Beaver Acres Roofing - From BCA	TBD										
	\$ 1,581,933	ф Б 704 000									
Net Balance		\$ 5,781,933									

2014 Bond Program Financial Status Report Security Upgrades \$10,600,000 Budget

Security Upgrades		Work	Complete		Work or In		. pr-18 ② Comp.		//ay-18 @ Comp.	% Complete
					·					
Phase 1: Building Perimeter Secuity	Safety Committee Approved									
Group 1 Schools	2015	\$	1,546,672	\$	762,744	\$	2,309,416	\$	2,309,416	67%
Group 2a Schools	2016	\$	1,807,930	\$	428,891	\$	2,236,821	\$	2,236,821	81%
Group 2b Schools	2017	\$	3,067,434	\$	-	\$	3,067,434	\$	3,067,434	100%
Group 3a Schools	2018	\$	-	\$	1,470,724	\$	1,470,724	\$	1,470,724	0%
Group 3 Schools Balance	2019-2020	\$	-	\$	5,402,992	\$	5,402,992	\$	5,402,992	0%
Security Projects Total		\$		\$	8,065,351	\$	14,487,387	\$	14,487,387	
- County Frojecto Fotal		Ψ		7	3,000,001	<u> </u>	,-01,001	7	. 1,401,001	

The current project budget is fixed at \$10,600,000. The purpose of this sheet is to demonstate the total estimated cost (design and construction) to complete building perimeter security upgrade needs. The current Est @ Comp. is based on bid results received for the summer 2017 assuming CM/GC procurement (not used in 2015 and 2016 work) and escalation through appropriate completion year.



2014 Bond Learning Technology/Classroom Systems and Critical Equipment Purchases April 30, 2018 Report


		Le	arning Techno	ology/Classroom	Systems - \$56 Million
	% Complete	Project To Date Expenditures	2017-18 Budget	2017-18 Expenditures as of 4/30/18	Annual Description of Expenditures
Networking Upgrades \$9,132,995	56%	\$ 5,125,444	\$ 369,082	\$ 61,532	Enterprise wireless upgrades complete. Maintaining current capacity and addressing specific use cases.
Digital Curriculum Development \$5,306,829	49%	\$ 2,386,283	\$ 591,871	\$ 471,325	Salary for six curriculum developers (5.0 FTE); Payment for TeacherSource Enhancements on the professional development module and Lesson Plan design.
Future Ready Schools \$31,513,097	51%	\$ 15,982,771	\$ 2,242,734	\$ 1,312,407	Initial device deployment compelte with Chromebooks 1:1 in grades 4-12 and iPads 3:1 in grades K-3. Evaluation process beginning to select devices for years 5-8 of the bond.
Technology Modernization \$2,961,479	50%	\$ 1,490,355	\$ 1,176,538	\$ 405,414	Data Center design complete and installation in process. Business Continuity process complete and working on yearly update. Security improvement implementation in process.
Other Technology/ Curriculum Projects \$7,085,600	95%	\$ 6,764,505	\$ -	\$ -	Completed Technology/Curriculum Projects. Includes: student laptop replacements in 2014-15, high school science technology in 2015-16, positive change grants 2014-15 through 2016-17
Total Total Bond Funds Remaining	57%	\$ 31,749,358	\$ 4,380,225	\$ 2,250,678 \$ 24,250,642	



2014 Bond Learning Technology/Classroom Systems and Critical Equipment Purchases April 30, 2018 Report

	0/	Project To		Critical Equipment - \$24 Million												
•	% Complete	Date Expenditures	2017-18 Budget	2017-18 Expenditures as of 4/30/18	Quarterly Description of Expenditures											
Buses \$16,000,000	64%	\$ 10,212,979	\$ 2,031,836		Approximately \$2 million/year over eight years. In first year, \$4.25 million will be spent and \$2million/year will be spent in years two through seven. \$0 will be spent in the eighth year.											
Copiers \$3,020,354	31%	\$ 1,120,252	\$ 101,252	\$ 1,150	Approximately \$375,000/year over eight years.											
Classroom Furniture \$3,237,179	53%	\$ 1,397,733	\$ 160,000	\$ -	Furniture, fixtures & equipment, including technology, for full day kindergarten and additional teachers K-5.											
Athletic Equipment \$221,737	16%	\$ 35,235	\$ 206,502	\$ 20,000	Approximately \$100,000/year over three years beginning in year 2. \$75,970 was transferred in year 2 to the Scoreboard Replacements Project.											
Maintenance Equipment \$600,000	68%	\$ 405,123	\$ 172,961	\$ 153,084	Approximately \$120,000/year over five years beginning in year 2. Year 2 will have \$185,000. Year 6 will only have \$55,000.											
InTouch Printers \$5,586	93%	\$ 5,586	\$ 5,586	\$ 5,586	One time purchase of printers for new online receipting system at all levels.											
Other Equipment Purchases \$915,144	100%	\$ 915,143	\$ -	\$ -	Other critical equipment purchases as needed. Purchase of \$15,000 towards new locker banks at Stoller in 14-15, \$250,000 towards new musical instruments in 14-15 and 15-16, \$184,050 for cafeteria table replacements in 15-16, \$344,973 for high school scoreboard replacements in 2015-16 and 2016-17 and \$121,066 towards BSD's portion of shock pad installation at SW Quadrant Park with THPRD in 2016-17.											
Total Fotal Bond Funds Remaining	59%	\$ 14,092,051	\$ 2,678,137	\$ 2,179,576 \$ 9,907,949												



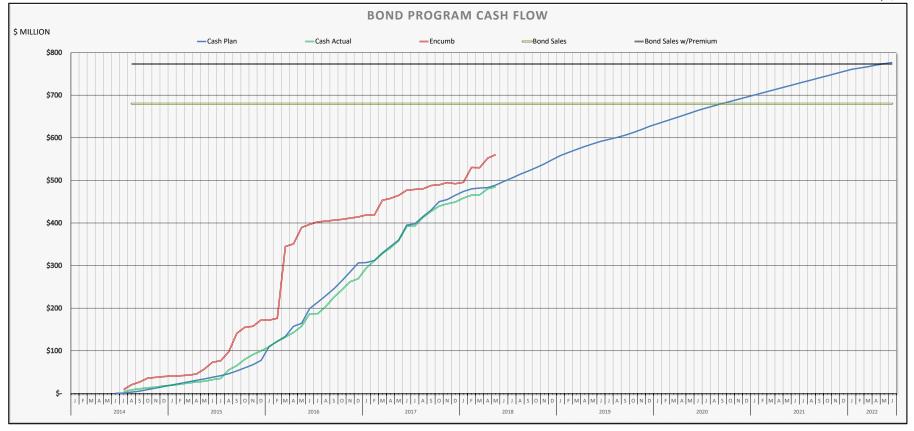



Hazeldale Elementary Construction Update

Information from the Beaverton School District

May 2018

Watch our progress on the time-lapse web cam: http://www.dwpwebcams.com/hazeldale/

Work Completed:

- · Boiler room work
- Water heater installation
- Vapor barrier installation
- Courtyard metal installation

Work Underway:

- Concrete for playground footings
- Casework installation in the north classrooms
- Drywall and taping in the south classrooms
- Sheet metal panel installation
- Roofing



Water heaters



Playground footings

General Contractor: Kirby Nagelhout

Architect: DLR Group

Substantial Completion: July 2018



Aerial view looking east



School bus loop



Classroom
